

AD-A158 828

ANALYSIS OF LOW BIDDING AND CHANGE ORDER RATES FOR NAVY
FACILITIES CONSTRUCTION CONTRACTS(U) NAVAL POSTGRADUATE
SCHOOL MONTEREY CA J R ROSMOND JUN 84

1/1

UNCLASSIFIED


F/G 5/1

NL

END

FILED

276



MICROCOPY RESOLUTION TEST CHART
NATIONAL BUREAU OF STANDARDS-1963-A

2

NAVAL POSTGRADUATE SCHOOL

Monterey, California

AD-A150 828



THESIS

ANALYSIS OF LOW BIDDING AND CHANGE
ORDER RATES FOR NAVY FACILITIES
CONSTRUCTION CONTRACTS

by

James R. Rosmond

June 1984

Thesis Advisor:

D. C. Roger

DTIC
ELECTE
MAR 6 1985

S D

Approved for public release; distribution unlimited

85 : 02 25 066

DTIC FILE COPY

UNCLASSIFIED

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

REPORT DOCUMENTATION PAGE		READ INSTRUCTIONS BEFORE COMPLETING FORM																					
1. REPORT NUMBER	2. GOVT ACCESSION NO.	3. RECIPIENT'S CATALOG NUMBER																					
		A150828																					
4. TITLE (and Subtitle)		5. TYPE OF REPORT & PERIOD COVERED																					
Analysis of Low Bidding and Change Order Rates for Navy Facilities Construction Contracts		Master's Thesis; June 1984																					
7. AUTHOR(s)		6. PERFORMING ORG. REPORT NUMBER																					
James R. Rosmond																							
9. PERFORMING ORGANIZATION NAME AND ADDRESS		8. CONTRACT OR GRANT NUMBER(s)																					
Naval Postgraduate School Monterey, California 93943																							
11. CONTROLLING OFFICE NAME AND ADDRESS		10. PROGRAM ELEMENT, PROJECT, TASK AREA & WORK UNIT NUMBERS																					
Naval Postgraduate School Monterey, California 93943																							
14. MONITORING AGENCY NAME & ADDRESS (if different from Controlling Office)		12. REPORT DATE																					
		June 1984																					
		13. NUMBER OF PAGES																					
		89																					
		15. SECURITY CLASS. (of this report)																					
		Unclassified																					
		15a. DECLASSIFICATION/DOWNGRADING SCHEDULE																					
16. DISTRIBUTION STATEMENT (of this Report)																							
Approved for public release; distribution unlimited																							
17. DISTRIBUTION STATEMENT (of the abstract entered in Block 20, if different from Report)																							
<table border="1"> <tr> <td colspan="2">Accession For</td> </tr> <tr> <td>NTIS GRA&I</td> <td><input checked="" type="checkbox"/></td> </tr> <tr> <td>DTIC TAB</td> <td><input type="checkbox"/></td> </tr> <tr> <td>Unannounced</td> <td><input type="checkbox"/></td> </tr> <tr> <td colspan="2">Justification</td> </tr> <tr> <td colspan="2">By</td> </tr> <tr> <td colspan="2">Distribution/</td> </tr> <tr> <td colspan="2">Availability Codes</td> </tr> <tr> <td>Dist</td> <td>Avail and/or Special</td> </tr> <tr> <td>A-1</td> <td></td> </tr> </table>				Accession For		NTIS GRA&I	<input checked="" type="checkbox"/>	DTIC TAB	<input type="checkbox"/>	Unannounced	<input type="checkbox"/>	Justification		By		Distribution/		Availability Codes		Dist	Avail and/or Special	A-1	
Accession For																							
NTIS GRA&I	<input checked="" type="checkbox"/>																						
DTIC TAB	<input type="checkbox"/>																						
Unannounced	<input type="checkbox"/>																						
Justification																							
By																							
Distribution/																							
Availability Codes																							
Dist	Avail and/or Special																						
A-1																							
18. SUPPLEMENTARY NOTES																							
19. KEY WORDS (Continue on reverse side if necessary and identify by block number)																							
Construction Contracts, Bidding, Change Orders, Fixed-Price Contracts.																							
20. ABSTRACT (Continue on reverse side if necessary and identify by block number)																							
One of the principal concerns of Government contract administration is the proper control of change orders. They are useful in resolving problems that would otherwise inhibit the satisfactory completion of contracts, but their overuse is an unnecessary drain on public funds. The purpose of this thesis is to evaluate what effects bidders of fixed-price Government construction contracts have on contract prices when the level																							

DD FORM 1 JAN 73 1473

EDITION OF 1 NOV 65 IS OBSOLETE
S N 0102-LF-014-6601

UNCLASSIFIED

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

UNCLASSIFIED

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

of competition intensity increases. It is suggested that in a climate of intense competition, the winners of bid awards are usually not only willing to assume the risk of losing profits, but also are willing to improve their financial positions through excessive use of contract change orders. This premise is tested against a sample of actual construction contract data from the Western Division, U. S. Naval Facilities Engineering Command. Several conventional measures of the level of competition intensity are applied in regression and variance analyses. *Author key words included:*

*8-8-61
Final 8/11/61*

10-10-14-14-14-14

UNCLASSIFIED

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

Approved for public release; distribution unlimited.

**Analysis of Low Bidding and Change Order Rates for
Navy Facilities Construction Contracts**

by

James R. Rosmond
Lieutenant Commander, United States Navy
B.S., University of Washington, 1974

Submitted in partial fulfillment of the
requirements for the degree of

MASTER OF SCIENCE IN MANAGEMENT

from the

NAVAL POSTGRADUATE SCHOOL
June 1984

Author: _____

Approved by: _____

Thesis Co-Advisor

Thesis Co-Advisor

Chairman, Department of Administrative Science

Dean of Information and Policy Sciences

ABSTRACT

One of the principal concerns of Government contract administration is the proper control of change orders. They are useful in resolving problems that would otherwise inhibit the satisfactory completion of contracts, but their overuse is an unnecessary drain on public funds. The purpose of this thesis is to evaluate what effects bidders of fixed-price Government construction contracts have on contract prices when the level of competition intensity increases. It is suggested that in a climate of intense competition, the winners of bid awards are usually not only willing to assume the risk of losing profits, but also are willing to improve their financial positions through excessive use of contract change orders. This premise is tested against a sample of actual construction contract data from the Western Division, U. S. Naval Facilities Engineering Command. Several conventional measures of the level of competition intensity are applied in regression and variance analyses.

TABLE OF CONTENTS

I.	INTRODUCTION	9
II.	BACKGROUND	12
	A. GENERAL	12
	1. Competitive Bidding	12
	2. The "Changes" Clause	14
	3. Change Order Rate	17
	B. CONTRACTOR PERSPECTIVE	19
	1. Bidding Strategy	19
	2. Measuring the Intensity of Competition	23
	3. Contractor Dislikes for Change Orders	25
	4. Contractor Preferences for Change Orders	27
	C. THE QUEST FOR PROFIT THROUGH CHANGE ORDERS	28
	1. Customer Requests	28
	2. Ambiguities of Contract Documents	29
	3. Value Engineering	33
	D. GENERAL HYPOTHESIS	33
III.	METHODOLOGY	35
	A. DEVELOPING THE DATABASE	35
	1. General	35
	2. Data Set Definition	36
	3. Refining the Data	38
	4. Summarization and Assumptions	39
	B. ANALYTICAL COMPUTATIONS	45
	1. Sorting, Rank-ordering, and Recoding of Data	46
	2. Mathematical Calculations	46

3.	Histogram and Plot Construction	46
4.	Regression Analysis	48
5.	Analysis of Variance	48
C.	FINDINGS OF ANALYSIS	48
1.	Dependent Variables	48
2.	Independent Variables	48
3.	Preliminary Findings	51
4.	Findings of Regression Analysis	52
5.	Findings of Variance Analysis	53
D.	SUMMARY OF ANALYSIS	58
IV.	SUMMARY AND CONCLUSIONS	60
A.	SUMMARY	60
B.	CONCLUSIONS	61
C.	FUTURE RESEARCH	63
	APPENDIX A: DESCRIPTION OF DATABASE VARIABLES	64
	APPENDIX B: WESTDIV CONSTRUCTION CONTRACTS DATA	68
	LIST OF REFERENCES	86
	INITIAL DISTRIBUTION LIST	89

LIST OF TABLES

I.	Summary of Distribution for Database Contracts . .	39
II.	MCON Contracts by Category Code	44
III.	Change Order Rate Summary	51

LIST OF FIGURES

2.1	Construction Contract Changes Clause	15
2.2	Construction Unemployment Fiscal Years 77-82 . .	24
3.1	Construction Industry Inflation, Fiscal Years 1977-1982	47
3.2	Histograms of Change Order Rates	49
3.3	Plot of Change Order Rate vs. Bid/Govt Est . . .	54
3.4	Variance Analysis for Geographical Areas	56
3.5	Variance Analysis for Bid/Govt Estimate	57

I. INTRODUCTION

The U. S. Government enters into a large number of contracts with the private sector because it has an interest in encouraging private action to accomplish its goals. Contracts are written, agreed to, and executed with the purpose of fulfilling the needs of Government agencies. In doing so, however, many contracts experience cost overruns because of imperfect wording of contract provisions, technical difficulties experienced by contractors, changes in Government mission requirements, or other reasons.

One cause of cost overruns is the change order--a modification issued unilaterally by a Government contracting officer directing the contractor to make changes within certain regulatory limits. The change order is issued during the life of the contract and usually directs certain actions in exchange for compensation to the contractor. The intent of the change order is to benefit both the Government and the private contractor in seeking equitable solutions to otherwise untenable situations. The change order is considered a tool of the Government to provide flexibility during contract administration, but its value is fully realized only when used with restraint. Contract managers sometimes permit change order to be used excessively, especially when they make liberal or lenient interpretations of change order regulations and policies.

The contractor is motivated by the need to survive and to make profits. It is understandable that changes to a contract would be priced at a premium if the prices were solely determined by the contractor, so payments for changes are negotiated at what is considered to be "equitable

adjustment."¹ Critics of Government overspending cite instances of wasteful overruns on Government contracts as testimony to the mismanagement of funds. It is the Government's duty to use these funds strictly for the public good. Since private concerns are subordinate to the public good, the Government has an equal interest in assuring that private individuals do not benefit at its expense.

The process of cost overruns may be exemplified in Government construction contracting by significant numbers of change orders. Construction contracting is unique because virtually every facility differs from others in terms of function and description. Whenever a new and creative architectural concept is expressed in a set of drawings and specifications, it is difficult to insure that all the details are flawlessly coordinated.

This thesis will analyze problems associated with change orders for construction contracts and attempt to identify variables that significantly affect change order occurrences. The motivation of contractors is of primary concern in determining whether they have been successful in attaining profits and in improving their positions as a result of overreliance on changes to contracts.

Chapter II provides a background for the concepts of competitive bidding and contract change orders. A perspective of the bidding contractor is taken to examine his motives and strategies prior to bidding. Several measures of "level of competitiveness" are introduced from bidding theory literature that will be employed in the analysis chapter of this thesis. The means by which change orders

¹The determinant of what constitutes an "equitable adjustment" has never been objectively qualified or quantified. It is construed in the ordinary meaning to connote a "fair," "reasonable," "just," or "right" arrangement or settlement.

can be made are examined. The general hypothesis of this thesis is then presented after the reader is introduced to these concepts.

Chapter III is the presentation and analysis of a model constructed of actual data from one of the Naval Facilities Engineering Command's (NAVFAC) Engineering Field Divisions (EFD). Recently awarded construction contracts of Western Division, Naval Facilities Engineering Command (WESTDIV) are analyzed using the concepts introduced in Chapter II. Appendices A and B provide a description and listing of the variables used for the analysis.

Chapter IV summarizes the thesis and the findings discovered in analysis. In addition, some general conclusions are made which are either supported by the findings or which attempt to explain inconclusive results. Finally, recommendations for future, related research are made.

II. BACKGROUND

A. GENERAL

1. Competitive Bidding

The Department of Defense (DOD) is the largest contracting agency in the federal government, with annual awards running well over \$100 billion in the early 1980's. By the end of the decade this figure is likely to double. Congress and others concerned with federal spending and accountability have paid particularly close attention to DOD because most of this money is spent noncompetitively. In Fiscal Year 1981, of \$105.2 billion worth of prime contracts, only 7.6 percent of this money was involved in competitively-awarded contracts [Ref. 1: p. 106].

This concern generated the creation of the Office of Federal Procurement Policy as an agency to prescribe regulations and policies for federal procurement that would foster more competitive pricing [Ref. 1: pp. 241-245]. The Federal Budget in 1982 projected total government outlays for shore facility construction and rehabilitation in excess of \$30 billion [Ref. 2: p. 1]. The Navy Department's share of this amount was approximately \$830 million.² The Naval Facilities Engineering Command (NAVFAC), which administers most of this money, traditionally awards its construction contracts on a competitive, lump-sum basis. Competitive procurement then, is a consistent practice among the few.

²The Federal Budget projected this amount for Fiscal Year 1982 Navy Department Military Construction outlays. This included money for for active and reserve Navy and Marine Corps components. It did not include construction funded from other sources, such as Non-Appropriated Funds, Defense Family Housing, and Operations and Maintenance appropriations.

Competitive bidding, however has not escaped criticism. Former General Counsel for the Department of the Navy F. Trowbridge Vom Baur once argued during a Senate hearing that fierce competition is not in DOD's interest because it forces contractors to offer "bare bones" prices that could cause them to go out of business. As a result the contractor, Vom Baur stated, is forced to find a way to recover any foregone contingency for claims after the contract is awarded. This could be done he claimed, as a result of changes desired by the Government during the performance of the contract work. Furthermore, he contended that competitive procurement attracts only "marginal producers" interested in low profit business. Referring to complex systems procurement, he explained that claims would occur more often when contracts are competed than when they are negotiated. [Ref. 3: pp. 120-121]

A supporting argument is that the competitive bidding process carries with it a heavy financial burden on the Government and spawns some ridiculous practices. "Competitive bidding causes government to be a bad customer and, therefore, get bad treatment from the vendor." The contractor is obliged to cut services where possible and act particularly stingy and uncooperative when the contractor learns that some significant feature or requirement was left out of the original contract documents. [Ref. 4]

Ample testimony has been given to refute the criticisms of competitive bidding [Ref. 5]. Senator Proxmire challenged Vom Baur's statements with convincing counterargument. Nevertheless, a competitively bid, fixed price contract imparts more risk upon a contractor than any other common form of contractual agreement. The "Changes" clause in Government contracts was therefore adopted for the mutual benefit of the contracting officer and the contractor [Ref. 6: p. 38].

2. The "Changes" Clause

The concept that the Government should have the right to order changes to the work under a contract has been a part of the Government contracting process for years. The "Changes" clause (see Figure 2.1) gives the Government the flexibility to purchase work or effort directly from an existing contractor without the necessity of following the statutes which require procurement pursuant to the formal advertising method. Provided a change is "within the general scope of the contract," a Contracting Officer may bypass a great deal of administrative effort by negotiating the cost of a work change directly with the original contractor.³

The "Changes" clause also serves a useful purpose in allowing contractors a means of initiating changes when errors in the drawings and specifications or special problems in site conditions are encountered. Some Government officials have been concerned that a contractor can utilize this clause as a vehicle for improving his position under a contract where a loss is being incurred either because of a substantial underbid or a variety of other reasons. The contractor is in a strong bargaining position knowing that there will be no price competition. [Ref. 6: pp. 38-39]

A "Changed Conditions" clause was originally incorporated into the Armed Services Procurement Regulation (ASPR)⁴ to discourage construction contractors from

³A change order will be defined herein as a means of ordering variations, changes, and additions to the work under contract within the normal authority of the NAVFAC Engineering Field Division. Therefore Supplemental Agreements and change orders that, when added to existing change orders on a contract, exceed one hundred percent of the original contract price shall not be included. Field ROICC's are not authorized by NAVFAC to exceed this percentage.

⁴The ASPR, adopted in 1947, was replaced by the Defense

**STANDARD FORM 23-A CONSTRUCTION CONTRACT
CHANGES CLAUSE**

CHANGES (1968 FEB)

(a) The Contracting Officer may, at any time, without notice to the sureties, by written order designated or indicated to be a change order, make any change in the work within the general scope of the contract, including but not limited to changes:

- (i) in the specifications (including drawings and designs);
- (ii) in the method or manner of performance of the work;
- (iii) in the Government-furnished facilities, equipment, materials, services, or site; or
- (iv) directing acceleration in the performance of the work.

(b) Any other written order or an oral order (which terms as used in this paragraph (b) shall include direction, instruction, interpretation or determination) from the Contracting Officer, which causes any such change, shall be treated as a change order under this clause, *provided* that the Contractor gives the Contracting Officer written notice stating the date, circumstances, and source of the order and that the Contractor regards the order as a change order.

(c) Except as herein provided, no order, statement, or conduct of the Contracting Officer shall be treated as a change under this clause or entitle the Contractor to an equitable adjustment hereunder.

(d) If any change under this clause causes an increase or decrease in the Contractor's cost of, or the time required for, the performance of any part of the work under this contract, whether or not changed by any order, an equitable adjustment shall be made and the contract modified in writing accordingly: *Provided, however,* That except for claims based on defective specifications, no claim for any change under (b) above shall be allowed for any costs incurred more than 20 days before the Contractor gives written notice as therein required: *And provided further,* That in the case of defective specifications for which the Government is responsible, the equitable adjustment shall include any increased cost reasonably incurred by the Contractor in attempting to comply with such defective specifications.

(e) If the Contractor intends to assert a claim for an equitable adjustment under this clause, he must, within 30 days after receipt of a written change order under (a) above or the furnishing of a written notice under (b) above, submit to the Contracting Officer a written statement setting forth the general nature and monetary extent of such claim, unless this period is extended by the Government. The statement of claim hereunder may be included in the notice under (b) above.

(f) No claim by the Contractor for an equitable adjustment hereunder shall be allowed if asserted after final payment under this contract.

Figure 2.1 Construction Contract Changes Clause.

including contingency allowances in bids for additional work possibly experienced in handling subsurface materials. It promised an equitable adjustment in contract price for additional work necessary to deal with unforeseen conditions. It could be employed only where both contractor and Government parties labor under a "mutual mistake of fact" concerning estimates or beliefs involved. Therefore, it was not the purpose of the Changed Conditions Clause to protect a contractor from his own errors of judgment or calculations. [Ref. 7: p. 19]

In 1968, a slightly revised clause was adopted dealing with "differing site conditions." This clause is incorporated into the General Provisions for Construction Contracts. In effect, this clause removes some risk from the Government by providing for an adjustment decreasing the price if the conditions are found to be better than expected. "Differing Site Conditions" replaced the former title "Changed Conditions" in the Standard Form 23-A (Contract Provisions for Construction Contracts) to describe more accurately the subject matter of the clause. [Ref. 8: p. 205]

There is no question that the "Changes" clause has been used for the purpose of improving the contractor's position. The Government has several ways to protect itself in this situation. The most common is to require adequate proof of claimed increased costs [Ref. 6: p. 39]. In general, the Government is insulated from contract price growth by explicit federal regulations binding contracting parties and policies that discourage excessive change orders.

Acquisition Regulation (DAR), which has since been consolidated into and replaced by the Federal Acquisition Regulation (FAR). The provisions for Changed Conditions, stated within, are still applicable as 10 U.S.C. 2301.

3. Change Order Rate

The change order rate is simply the percentage increase (or decrease) in contract price over the original award amount due to change orders. It is used specifically in this research to assess the impact of price changes irrespective of contract size. It has the advantage of placing all contracts under a normalized measure of performance. The corresponding disadvantage is that a given change order rate may have very different impacts on contracts of contrasting size. This raises the question whether the change order rate is a useful measure for assessing the performance of contract administration. For example, a ten percent increase in contract price for a small contract may be the result of one rather mundane change. A ten percent increase for a large contract, however, probably is the result of more complex problems for the contractor. The amount for these changes could involve complex construction methods that affect other portions of work, or the amount could be an accumulation of many minor changes. A number of small changes as opposed to a single larger one, has the tendency to spread disruptive effects throughout many phases of construction. This problem has been the subject of claims made by contractors for "impact" costs created by a "ripple effect," where a change disrupts the remainder of the contract work [Ref. 9: p. 46].

Keeping contract change orders within controlled minimums is one of NAVFAC's goals [Ref. 10: p. C-109]. Any realistic limit to change orders must be expressed as a goal, not an absolute. Many change orders are valid and prudent tools for accomplishing mission objectives. They are issued for various reasons, including correcting any errors or omissions in plans and specifications. They give the Government the flexibility to make convenient adjustments as

a result of inevitable errors, oversights, and changes in conditions or requirements. Yet Government agencies have been accused of using change orders excessively [Ref. 11: p. 8]. Criticism has been focused on proper or sufficient actions by Government Contracting Officers to:

- Ensure the correctness of contract documents prior to the solicitation of the invitation for bids.
- Screen nonessential customer-requested change orders.
- Settle contract change order prices within reasonable amounts during negotiations with contractors [Ref. 2: pp. 9-14].

NAVFAC communicates specific management goals for its subordinate Engineering Field Divisions (EFD's) through annual Command Management Plans (CMP). In many cases, goals are specifically tailored for each EFD. Under the Fiscal Year 1984 Construction Program of the CMP, all EFD's are subject to the same criteria for change orders:

- Keep all construction type change orders within six (6) percent of their cumulative current year contract Work in Place⁵ (WIP) while maintaining Military Construction change order activity at five (5) percent.
- Keep unforeseen conditions orders⁶ within two percent of the cumulative current year construction contract WIP.
- Keep design change orders⁷ within 1.5 percent of the cumulative current year construction contract WIP. [Ref. 10: p. C-109]

⁵Work in Place refers to the dollar value of work considered to be constructed in place by a contractor. Progress payments are entitled to the contractor based upon the determination of this value by the ROICC.

⁶CMS-coded (see Chapter III.A.1) change orders caused as a result of underground obstructions, changed soil conditions, unobserved site conditions and misstated underground utility locations.

⁷Change orders coded for design errors and omissions.

Internal controls to stem the abuses criticized above are incorporated into NAVFAC directives. Preprocurement actions are carefully delineated in NAVFAC's Contracting Manual (P-68) to assure comprehensive review of contract documents prior to award. The negotiation of change order prices requires an independent Government estimate to be used as the basis for determining a reasonable settlement. Customer-requested change orders must be limited to "in scope" changes with the stipulation that "desirability of the change and the fact that funds may be available do not enter into determinations of scope" [Ref. 12: p. 7-3.1.]. Before the construction plans and specifications are disseminated to prospective contractors, there are three stages of design review. The first two stages are reviews by NAVFAC managers to insure that designs and specifications are adequate for the intended construction. The last of these is a customer review to ensure that a facility will meet the stated functional and mission requirements [Ref. 13: p. 6].

B. CONTRACTOR PERSPECTIVE

1. Bidding Strategy

Contractors, over the long run, are forced to bid low enough to win, yet high enough to cover cost and make a profit. Successful strategy then, as depicted in bid theory, is to bid at a rate above cost that will yield the greatest expected value, that is, the net of probability of winning multiplied by profit margin. As profit margins are increased, the probability of winning is decreased. As a contractor successively increments his profit margin in a bid, he increases the probability that he will exceed the bid of one of his competitors--and therefore lose the award. Presumably, an optimal profit margin exists where the

corresponding probability of winning an award yields the greatest expected profit [Ref. 14: pp. 488-490].

The contractor's first prerequisite for making profits is to win a bid. In the short run, a contractor may be compelled to use a low bid strategy that virtually assures his chances of winning. The amount of his winning bid can seem quite illogical to other competitors. A common occurrence that has frustrated many contractors is that many of the bids submitted on all types of projects appear to be below reasonable costs. In one particular observance, nearly 80 percent of the bids on all major jobs were at less than the engineer's estimate,⁸ some even at less than half the engineer's estimate [Ref. 15: p. 127]. In Government contracting, the mandatory independent estimate of project costs is an average cost only. In contrast, bids of rival firms on contracts represent opportunity costs for their resources. Each rival firm has the option to choose those contracts that are the most advantageous to them in terms of their special qualifications. These low bids are indicative of marginal costs. A Government estimate cannot be contractor specific, that is, representing the cost of performing a particular project or job for one specific firm [Ref. 16: p. 214].

It is advantageous for the contractor to consider the following in choosing a job so that he will have a likely chance of winning:

- a. Size. Usually the larger the job, the fewer will be the number of competitors. This increases the probability of winning. Adversely, the larger the estimate, the greater the risk that the estimate will be

⁸The independent estimate made by the architect-engineer as an agent of the owner. For Government contracting the parallel is the Government estimate.

inaccurate. Larger construction projects tend to involve more unconventional construction methods and have many interrelated activities. Estimators are more prone to errors and oversights in determining the costs for these methods or activities. Smaller jobs may be more attractive to contractors as they can be the foundation for invaluable contacts and reputation for later, more profitable eventualities--a form of advertising.

- b. Care and attention required. A smaller organization may be more successful in performing work on a job that requires more attention to detail than could be provided by a large, high-overhead company.
- c. Profit advantage. Several jobs concentrated in one locality offer inherent advantages. Economies of scale can be realized for labor, materials, and supervision. Improved labor relations and productivity, price discounts for bulk purchases, and improved time-saving and coverage of supervision and management result.
- d. Continuity of employment. Steady employees earn their pay more productively. Once the maximum yearly contribution to the Social Security tax (FICA) has been made by the contractor, the balance stays with the contractor as a distinct accrual to his job return.
- e. Labor conditions. Jurisdictional disputes may involve a contractor's workforce and result in wage increases.
- f. Subcontracting. The reaction and bid of the subcontractor can be important. If the contractor can be assured of obtaining low subbids from reliable subcontractors, he will have a good chance of getting profitable work.

- g. Financial solvency. The competitive edge may be determined by the ability to finance construction between progress payments, procure construction and payment bonds, and take advantage of trade discounts for prompt payment.
- h. Competition. The greater the number of competitors, the lower the contract price must be to win the award. A decrease in price below a certain point makes opportunities elsewhere more favorable. [Ref. 17: pp. 81-86]
- i. Seasonal considerations. Some contractors disregard overhead and equipment costs and bid low upon reaching a certain volume of work during an operating year.
- j. Desperation. When a contractor is in a financial position where money is urgently needed to pay bills, any source, including jobs at a loss, can prolong survival in business [Ref. 15: pp. 187-188]. When faced with a choice of giving up his capital to avoid going deeply into debt, a contractor will assume a great amount of risk just to stay in business. [Ref. 18: p. 154]

There is an intuitive reason to suspect that a winning bid is occasionally submitted by a poorly-informed, irresponsible bidder. The poorly-informed bidder cannot expect to make a positive profit since his bid must undercut an amount very close to the project's "true value" in order to win. The "true value" is a theoretical estimate of what the project should cost, after all biases for misjudgment of costs, unreasonable contingency amounts, and greed are removed. The poorly-informed bidder, in order to make any profit at all, must bid within a very narrow interval between this "true value" and the maximum-informed bidder's amount. More likely, his winning bid will be below the

"true value." This phenomenon is referred to as the "winner's curse;" the individual to whom a contract is awarded tends to be the one who most underestimated the true value of the work [Ref. 19: p. 133]. In higher-risk contracts, the Government might award the contract to a contractor of questionable financial stability, but who cannot be classed as irresponsible.⁹ Reputable contractors would avoid such high-risk, lump-sum contracts, because they would expect to be underbid by contractors who fail to see risk or who desire such risk [Ref. 18: p. 154].

All contractors must face risk. Risk includes all exposures to loss brought about by nature, organizational shortcomings or outside influences. Some of these are: (1) weather, (2) unexpected job conditions, (3) personnel problems, (4) delays in material deliveries, (5) labor strikes, (6) faulty materials, (7) faulty workmanship, (8) operating problems (additional expenditures for increased supervision, damage to equipment through overloading or poor maintenance), and (9) natural disaster.

Successful bidding strategy would seem to involve a careful synergism between assumption of risk and assessment of competition. A misjudgment of the former is likely to result in a disastrous financial consequence. Misjudgment of the latter will likely result in loss of the award.

2. Measuring the Intensity of Competition

A sharp increase in construction industry unemployment occurred in the spring of 1980 (see Figure 2.2). The industry recession prompted contractors to be much more competitive as demonstrated by contractor practices in soliciting business on a national rather than strictly local

⁹If considered a "responsible" bidder, a contractor is entitled to award provided he is also a responsive bidder.

scale, bidding on new types of work, and bidding more projects. Officers of several reputable firms lamented that in order to win, profit margins in bid estimates had to be cut between 25 and 50 percent. [Ref. 20: p. 70]

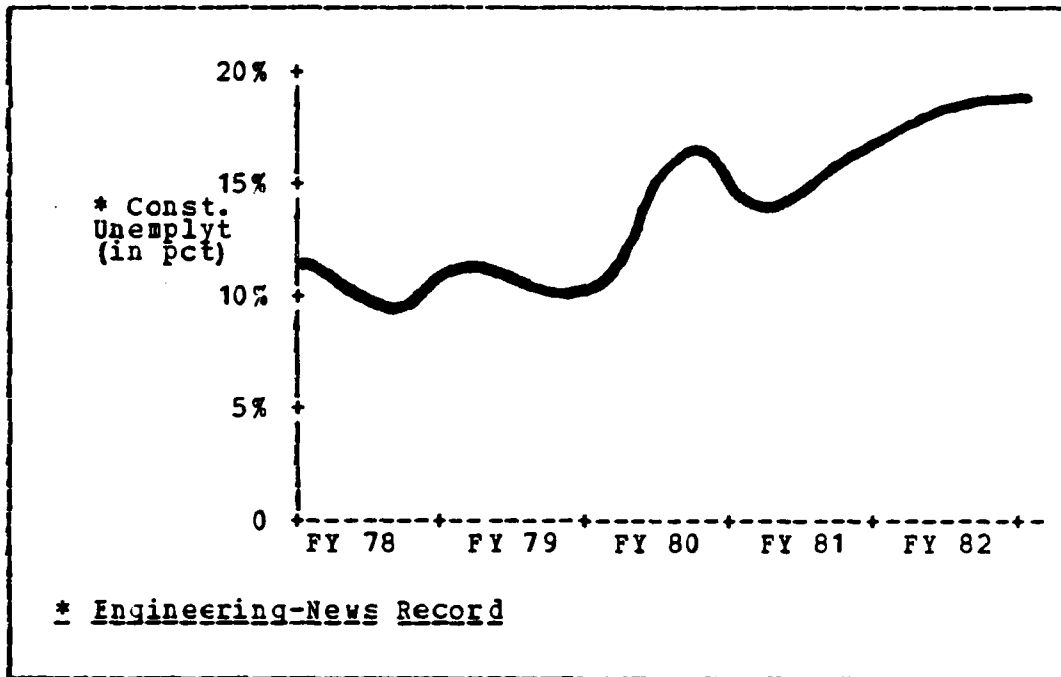


Figure 2.2 Construction Unemployment Fiscal Years 77-82.

The level of competition for a particular contract can be measured in at least three ways. First, the spread, or difference between the low bid and the second low bid, measures the amount of money "left on the table" and indicates how much higher the low bidder could have been and still taken the award. As the number of bidders increases, the percentage spread decreases [Ref. 21: p. 1382]. Second, the ratio of the winning bid to the Government estimate can be used. A ratio near one would indicate firms bidding near average costs while a lower ratio would indicate more

competitive opportunity costs [Ref. 16: p. 214]. The third measure, the expected number of bidders, can be applied where it is necessary to decrement one's markup margin (in order to win) as more competitors respond to the invitation for bids [Ref. 16: p. 213].

The spread can be normalized for contracts of varying sizes by expressing it as a percentage of difference between the lowest and second lowest bids. The bid-to-Government estimate ratio is already normalized and the number of bidders does not appear to be significantly related to the size of a contract. [Ref. 16: p. 217]

An analysis conducted for a large general contractor illustrates that winning bids are based on opportunity costs. Over a two year period, 35 percent of all competitors' bids were below this contractor's estimated direct "out of pocket" costs of performing the work. This contractor was still able to compete successfully among other reputable firms, and his estimates closely reflected his actual costs of operation. Two-thirds of all bids submitted by his competitors fell between 91 and 120 percent of his direct job cost. To be assured a 50 percent probability of winning each award, the contractor would have had to bid below construction cost, or at a negative profit. [Ref. 15: pp. 127-128]

3. Contractor Dislikes for Change Orders

Many contractors contend that change orders are unprofitable [Ref. 22: p. 314]. They complain that they require great effort to price and then take considerable time to get approved and processed [Ref. 23: p. 8]. The implementation of changes results in a dilution of top supervision on original contract work. Too much time of key individuals is spent arranging for changes and pricing and negotiating them [Ref. 9: p. 46].

This sentiment may partially explain why complaints arise from the Government that change orders are priced too highly by contractors. The contractor attempts to account for unknown costs which he fears may occur, while Government estimators may have an unrealistic understanding of actual costs involved in certain operations, particularly the low productivity of direct labor as a result of changes, delays, and uncertainties [Ref. 9: p. 47]. Those contractors averse to change orders should be logically in favor of contracts that limit the amount of damages entitled to the contractor, some contract administrators argue [Ref. 24: pp. 97-98]. If the Government is lenient in permitting compensation to contractors for disputed matters where liability is questionable, then disreputable contractors will benefit. The disreputable contractor, who relies on these compensations, will underbid honest contractors. Limitation of liability clauses in a contract would stem the practice of bidding low and seeking to recoup losses at a later date [Ref. 24: pp. 97-98].

The additional financial burden of performing change orders may be unaffordable to the contractor who is in a low cash position. The contractor also must deal frequently with "constructive"¹⁰ change orders, which are informal but have the effect of eroding profits. A contractor may incur losses on a contract unknowingly, suspecting that there are deficiencies in his accounting system. The real problem may be unidentified constructive change orders [Ref. 25: pp. 5-6].

¹⁰An oral or written act or omission by the Contracting Officer or other authorized Government official which is of such a nature that it is construed or inferred to have the same effect as a formal written change order under the "Changes" clause.

4. Contractor Preferences for Change Orders

Since the Government reserves the right to issue "in-scope" changes to the provisions of a contract, the contractor is within his rights to demand equitable adjustments for additional costs anticipated in associated extra work. If a change reduces the amount of work under contract, the Government, too, is usually entitled to consideration through a reduction of contract price. U. S. Navy contracts ordinarily permit a limit of six percent profit for changes negotiated pursuant to the "Changes" clause [Ref. 12: p. 7.3.4]. The claim that Government estimators of change order prices have been too reliant upon contractor estimates during negotiations [Ref. 11: p. 28], raises the question whether this profit limit has been frequently circumvented. Furthermore, the profit that might have been realized through these changes may have been of sufficient amount to improve many contractors' faltering financial positions.

The practice of trying to obtain a contract award by knowingly offering a price less than anticipated costs, with the expectation of increasing the price during performance through change orders, is referred to as "buying in." This is generally deemed to be irrational bidding behavior for contractors, except for large, multibillion-dollar firms that depend upon traditional growth in defense "state of the art" programs [Ref. 1: p. 106]. But "buying in" may not seem so irrational if viewed as a two-part strategy. Behind the low bid could be a "bail-out," or contingent escape strategy. A "bailout" is a loophole which allows the bidder to recoup losses. The "bail-out" can even be perpetrated with the help of the Government by accepting whatever the contractor can deliver, even if it is a cheaper or substandard product. After all, it is reasoned, the public

disclosure that a very low bid has been accepted could be ultimately embarrassing to Government officials. Either a deductive change order or termination of contract, which would have the effect of minimizing the contractor's losses, could be a satisfactory compromise for both parties [Ref. 26: pp. 84-87].

C. THE QUEST FOR PROFIT THROUGH CHANGE ORDERS

The potential to profit from any change order depends upon many factors. Among the most prominent of these is the type of change order. The Defense Audit Service, in a 1982 audit [Ref. 11: p. 8], attributed 73 percent of DOD change orders to three causes. Slightly over half of the change orders they found were due to deficiencies in designs and specifications; ten percent resulted because specifications and designs had not been completed before the basic contracts were awarded; and about eleven percent of the change orders were the result of user requests for changes. Value engineering changes were not cited as a significant cause of change orders, but they are very attractive for enhancing contractor profitability.

1. Customer Requests

It is difficult to predict customer-requested change orders since they are implemented either in response to unpredicted changes in mission requirements, or in as a result of inadequate planning. They can be generated as a real facility need or as a compromise or exchange for facility features no longer required. It has been an implicit policy of NAVFAC to accommodate the customer's desires for such changes [Ref. 11: p. 19]. If the contractor is bound by a set of explicit specifications and drawings, the customer-requested change order may be one of

the final avenues for opportunity profits. An indicator of contractor motive here would be seen by suggestions for changes made by the contractor directly to the facility user.

2. Ambiguities of Contract Documents

The most overt evidence of contractor motive to benefit through change orders has been seen in the litigation of disputes over contract documents. Considerable legal precedent in establishing the conditions through which a contractor may benefit from contract ambiguities has evolved in the courts. A number of landmark cases clearly shows that both Government and contractor parties cannot use unilateral interpretations of contract language to benefit at the expense of each other. Since the majority of change orders are caused by mistakes in the preparation of contract documents, this is the most fertile ground for seeking extra compensation. Ordinarily the contractor relies on the implied suitability of Government plans and specifications for their intended use [Ref. 27: p. 1076]. But a contractor's interpretation of contract language may differ from that of the Government's due to some degree of ambiguity caused by imperfect wording, conflicting statements or depictions, or connotated meanings. The legal system has tested many cases involving contract ambiguities and has, as a result, produced two counterbalancing, risk allocation principles: the rule of contra proferentum, which adopts the interpretation that favors the non-drafting party (contractor) and the rule of pre-contract clarification, which denies adoption of a contractor's interpretation when he has failed to request clarification of an ambiguity of which he knew or should have known [Ref. 27: pp. 993-994].

a. Legal Precedent Favoring the Contractor

Courts have generally been sympathetic to contractors when inaccurate or incomplete information in bid packages result in unexpected costs. In Peter Kiewit Sons' Company v. United States, 109 Ct. Cl. 390 (1947), the Court of Claims held:

Where one of the parties to a contract draws the document and uses therein language which is susceptible of more than one meaning, and the intention of the parties does not otherwise appear, that meaning will be given the document which is more favorable to the party who did not draw it. This rule is especially applicable to Government contracts when the contractor has nothing to say as to its provisions. [Ref. 6: pp. 231-232]

In WPC Enterprises, Inc. v. United States, 163 Ct. Cl. 1, 323 F.2d 874 (1963), and Blount Brothers Construction Co. v. United States, 171 Ct. Cl. 478, 346 F.2d 962 (1965), the Courts ruled that where an ambiguity was "subtle, not blatant" and where the contractor is genuinely misled and not deliberately seeking to profit from a recognized error by the Government, relief is entitled to the non-drafter [Ref. 28: p. 152]. Furthermore, in Gholson, Byars and Holmes Construction Co. v. United States, 173 Ct. Cl. 374, 351 F.2d 987 (1965), the Court ruled that there is no duty to seek clarification where a contractor innocently construes a subtle ambiguity in his favor. Equally important, if clarification is not provided to an ambiguity sought by a contractor, the Government will be held to have waived its right to complain of the interpretation placed on the contract by the contractor [Ref. 29: pp. 154-155].

Under the rule of pre-contract clarification, the contractor is obligated to inquire about major patent discrepancies, obvious omissions or drastic conflict in

provisions. In a case where the distinction between a patent and latent ambiguity was an issue, the Board of Contract Appeals in Worsham Construction Co., Inc., v. United States, GSBCA 5469, refused the Government invocation of the "patent ambiguity" rule as a means of preventing contractor recovery for a defective specification. [Ref. 30: pp. 9-10]

b. Legal Precedent Favoring the Government

The rule of pre-contract clarification is a rule of fair dealing which protects the Government from a contractor who intentionally submits a low bid with the goal of claiming ambiguities during contract performance to obtain price increases. In Beacon Construction Co. v. United States, 161 Ct. Cl. 1, 314 F.2d 501 (1963), the contractor failed to notify the Government of an ambiguity and interpreted the contract in its own favor. The contractor sought to recover expenses after performing the work where the contract language was vague. The Court denied relief to the contractor, holding that such a claim was made without protest and in absence of direction from the Government [Ref. 6: p. 234]. Where a conflict in contract documents exists and is known to the contractor, relief will be denied the contractor when he assumes the right to disregard the affected portions and apply his own remedy. The Court stated in S.O.G. of Arkansas v. United States, 212 Ct. Cl. 125, 19 G.C. (1976), that this action is taken to avoid post-award disputes of the type which arose here by encouraging contractors to seek clarification before anyone is legally bound [Ref. 31: pp. 3-4].

The pre-contract clarification rule also applies to circumstances where a reasonable or experienced bidder should be capable of recognizing a patent or glaring

discrepancy. In Wickham Contracting Co. v. United States, 212 Ct. Cl. 318, 546 F.2d 395 (1976), a contractor submitted a bid based on an erroneous drawing scale. The court ruled that the use of the erroneous scale was so unusual that it created a patent discrepancy [Ref. 27: pp. 1074-1078]. Similarly, in J. W. Bateson Co., Inc. v. United States, GSBCA 1221; R. M. Hollingshead Corp. v. United States, 124 Ct. Cl. 681, 683, 111 F. Supp. 285, 286 (1953); and others, the Courts generally agreed that:

An experienced contractor cannot rely on government-prepared specifications where, on the basis of the government furnished data, he knows or should have known that the prepared specifications could not produce the desired result for '... he has no right to make a useless thing and charge the customer for it.' [Ref. 27: p. 1079]

c. Misrepresentation

A contractor might receive relief or avoid the commitment to a contract if he is misled by a false representation or nondisclosure of terms in the bidding package. Although such action is usually not indicative of a contractor's motive to gain through changes to a contract, it provides recourse for a low bidder to escape an unprofitable dilemma. A Contracting Officer must be careful that he is not on constructive notice of an error where a mistake in bid is alleged after award of contract. If a low bid is significantly lower than other competing bids or the Government estimate, the contractor may avoid commitment to the terms of the contract ordinarily established under the firm bid rule¹¹ if he can demonstrate that the Contracting

¹¹Under the firm bid rule in Government contracting, the bidder cannot, in the absence of special circumstances, withdraw or revise a bid at the time of bid opening.

Officer had "constructive knowledge" of a mistaken bid.
[Ref. 32: pp. 152-153]

3. Value Engineering

Value Engineering changes are unique in that they tend to maintain the essential function of a facility while creating cost savings for both the Government and the contractor. Provided that a facility's "essential function" is retained intact, a Value Engineering change will deflate the change order rate and increase contractor profitability. In fixed-price NAVFAC contracts, the contractor's share of savings is determined by subtracting Government costs (resulting from developing and implementing the change) from contract savings and multiplying the result by 55 percent. The Value Engineering provision is applicable to contract prices of \$100,000 or more [Ref. 33]. Obviously it is an attractive alternative to consider for the change-minded contractor.

D. GENERAL HYPOTHESIS

It has been stated that contractors are compelled in competitive situations to bid very close to their expected costs of construction. They are motivated in some cases to win as a preferable alternative to having no business at all, even if it means operating at a loss. Winners of competitively-bid contracts are either those who enjoy the relative advantages of economies of scale or proprietary properties, or are willing risk-takers. Risk-takers are those who accept the probability of setbacks in the course of construction. More likely they probably believe that they can recoup profits later. Although there are many reasons that a prudent contractor would choose to avoid change orders, they are nonetheless inevitable. It is the

premise of this paper that there is a link between the cost of change orders to a contract and the degree of competitiveness under which that contract was bid. As bidding competition increases, those bidders who are more amenable to the risk of seemingly unprofitable ventures and are willing to gamble on change order dynamics displace the more conservative and reputable contractors.

The contractor can use a number of different change order types to his benefit. Among these are customer-requested changes, changes to correct mistakes and ambiguities in contract documents, changes to account for differing site conditions, and Value Engineering changes. Value Engineering changes have been shown to be a relatively small proportion of federal construction contract administration effort. If these contractors as described are typically successful bidders, then higher change order rates among contracts that are bid under strong competitive conditions should be systematically evident. Empirical data will be used in a model to test the following conclusions:

- A direct relationship exists between change order rate and degree of competition--measured by number of bidders, the "spread," bid/Government estimate ratio, bid/mean bid ratio, and deviation of winning bid from mean bid.
- Relationships exist among various classifications of construction contract change order rates according to: (1) timing of the contract award, (2) contract size, (3) geographical area, (4) type of facility, and (5) construction industry unemployment rate.

III. METHODOLOGY

A. DEVELOPING THE DATABASE

1. General

The data for the research were collected at the Western Division, Naval Facilities Engineering Command, San Bruno, California (WESTDIV). Only construction contracts that were formally-advertised and fixed-price are included for analysis. These contracts were WESTDIV administered--that is, advertised and awarded through WESTDIV or its authorized agents at WESTDIV-designated geographical locations. Therefore, construction contracts awarded by local Officers-in-Charge of Construction (OICC's) of more limited contracting authority at 20 remote "field" offices are not included.¹² The data were extracted from two sources:

- The Construction Management System (CMS), a subsystem contained in the AMALGAMAN/Integrated Disbursing and Accounting Data Base Master maintained by the Naval Facilities Support Office (FACSO). The information provided was extracted from the CMS system for the author. The data were transcribed from computer print-outs into the statistical computer program to be used for the analysis in this chapter.

¹²Navy Civil Engineer Corps officers assigned as Public Works Officers at Naval activities usually are assigned concurrently (dual authorities are vested in one person) as field OICC's. As a field OICC, contracting authority is more limited than that of the Commander of the Engineering Field Division (WESTDIV). Since field OICC contract bidding data are maintained locally at these remote offices and their collection was considered infeasible within the time constraint for research, they are excluded from analysis.

- Completed Scales of Bid Offers for Construction Contracts (12ND WESTDIV Form 4330/24) maintained by the Head, New Procurement Branch (Code 021) of the Acquisition Department. This information was provided by hardcopy listings of individual contract Government estimate and bid-opening results.

2. Data Set Definition

The model for analysis is established within the following considerations:

- Availability of bidding information.
- Recentness of information.
- Consistency in management policies concerning contract administration.
- Completion (closeout) of contract.
- U.S. Navy funding sources (appropriated and non-appropriated) only.

The major restriction for data analysis is imposed by availability of bidding information. Although CMS affords the opportunity to review award amounts and change order information for contracts of all appropriation sources and Engineering Field Divisions of NAVFAC, the extraction of information for bidding data and government estimates¹³ is cumbersome. Accordingly, only WESTDIV contracts awarded from Fiscal Year 1978 to the present have been included.¹⁴ This does afford relative currency of information. Fiscal Year 1983 data is excluded, however, due to (1) the small

¹³Government estimates for contracts are available in another subsystem of the AMALGAMAN Data Base, but they are not tailored as necessary to reflect the actual estimate for the base bid plus or minus the additive or deductive bid items that actually might have been awarded.

¹⁴Scales of Bid Offers are maintained at WESTDIV for six years until disposal. Coincidentally, data for completed contracts were implemented into CMS at the approximate starting point for this same period (1977).

proportion of completed contracts available and (2) revision of WESTDIV policies in (a) "downloading" many contracts to field OICC's (WESTDIV was authorized increases in manpower levels for field offices, so many contracts, especially CMW-funded, were delegated in 1983 to OICC's to administer), (b) accelerating the execution of WESTDIV contracts award phase and (c) encouraging other forms of modifications to contracts, such as Supplemental Agreements. Items (b) and (c) above were internalized in Fiscal Year 1983 WESTDIV management objective plans.

All considered contracts must have been "closed out" or completed, so that the change order rate is reflected as a final, static figure, rather than a dynamic one as under a contract-in-progress. This constraint is imposed so that all influences of contract price expansion during the life cycle of the contracts have matured.

Funding sources are limited to Military Construction, Navy (MCON) and Non-Appropriated Funds (NAF) contracts in excess of \$200,000, and Operations and Maintenance, Navy (OMN) contracts in excess of \$2500. This constraint is arbitrary. The intent is to view the incidence of construction change orders under one service branch (Navy), so that as much consistency in the attitudes and policies of making change orders could be ensured. This would avoid any possible biases by NAVFAC managers. The \$200,000 floor on MCON and NAF contracts reduces the size of this study's data base to a workable¹⁵ number and eliminates many mixed-funding source contracts.¹⁶ These contracts

¹⁵Initially it was estimated that inclusion of many smaller MCON contracts would overload the storage capacity of the MINITAB computing system used for statistical analysis.

¹⁶Many construction contracts are funded by a mix of more than one source-- for example, MCON and OMN dollars are commonly used under one contract for building alterations

represent a relatively small proportion of the total amount of MCCN and OMN funds administered by NAVFAC and therefore should not significantly bias the results of analysis.

3. Refining the Data

The data considered within the above constraints possess a number of clear outliers that, if included in the analysis, would distort overall values for change order pricing and bid averages. The following types of WESTDIV contracts are further excluded:

- Contracts terminated early, where the majority of construction dollars are not consumed or "in place." Otherwise the change order rate would appear as a large deductive (negative) one. A small number of contracts are terminated for convenience of the Government if the facility or some of its features are no longer required. A contract may also be terminated for default when the contractor fails to make satisfactory progress in construction or breaches the terms of the contract.
- Contracts for which costs listed in CMS do not account for the majority of the award amount. Presumably, other phases of construction had not yet been reported as completed or consisted of work funded under a separate, unreported source.
- Construction contracts for Adak, Alaska, under WESTDIV's cognizance; these contracts suffer from restrictive competition and unique logistics at an isolated location.

A total of 473 completed MCON, NAF, and CMN construction contracts awarded from October 1977 through September 1982 were listed on the CMS printouts as of 15

(MCON) and repairs (CMN) when the construction features for each funding source are clearly separated.

February 1984. Of these 47 were deleted for the reasons stated above. Another 126 contracts for Fiscal Years 1980 and 1981 were excluded because their corresponding Scales of Bids were not available. There remained 300 contracts for analysis. Table I summarizes the distribution of these contracts.

TABLE I
Summary of Distribution for Database Contracts

<u>FISCAL</u> <u>YEAR</u>	<u>NUMBER OF</u> <u>CONTRACTS</u>			<u>TOTAL DOLLAR AMT</u> <u>(in \$1000)</u>			<u>YEAR TOTAL</u> <u>(in \$1000)</u>
	CMN	MCON	NAF	OMN	MCON	NAF	
1978	6	43	4	\$ 868	72111	2453	\$ 75432
1979	28	76	6	6295	142980	5008	154283
1980	14	14	2	5741	31817	688	38246
1981	1	12	2	255	17645	569	18469
1982	60	28	4	14932	30279	1713	46924
	---	---	---	---	---	---	---
TOTAL	109	173	18	28091	294832	10431	\$ 333354

4. Summarization and Assumptions

Appendix A describes the variables provided for each WESTDIV contract by the Construction Management System and the Scales of Bids. Appendix B tabulates these data.

a. Assumptions

(1) Geographical Categorization.. To isolate the effects of geographical differences in climate, economy, employment rate, and other factors, the contracts are classified among eight general categories. Four of these pertain to major U. S. Naval activity concentrations, while the other four are classified as "rural" areas in the outlying vicinity of these concentrations. Generally these "rural" activities lie more than 50 miles or convenient commuting distance from San Diego, Los Angeles, San Francisco or Seattle/Emmerton.

(2) Number of Bids. It is apparent that some bids appearing on the Scales of Bids were disproportionately high as compared to either other competitors or the Government estimate. These bids would only distort values (such as standard deviation and mean bid) calculated for analysis [Ref. 21: pp. 1377-1378]. These are considered nonserious or "noise" bids and are typically excluded in studies of auctions and bidding models [Ref. 19: p. 126]. An appropriate algorithm for identifying these bids depends upon the model, and there appears to be no definite rule for determining them. Therefore, any bid greater than 150 percent of the competitive mean bid was arbitrarily considered a "noise" bid by the author and was extracted. This adjustment was made to 54 bids on 43 contracts. It was observed that some bidders consistently submitted "noise" bids. Common reasons for unreasonably high bid prices may fall into one or more of the following categories [Ref. 34: p. 127] :

- Complementary bidding. The bidder is not interested in performing the subject work, yet does not want to be otherwise prevented from bidding on future projects or to be deleted from future Bidder's Lists. The proposed

price is inflated to a range that will prevent likely award.

- Bidder error. Mistakes simply may be made when calculating bid prices.
- Bidder misunderstanding of the scope of the work.
- Perceived risk on the part of the bidder. Any number of factors may cause the bidder to perceive real or imaginary areas of risk and to raise his bid price to provide for this risk.
- The bidder may be quite uncertain about the proposed work, the Government's particular requirements of the contractor, or his ability to perform as expected.

(3) Next Lowest Bidder's Price and Spread.

The next lowest bidder's price and the spread are included for analysis to examine any significant relationships between change order rate and intensity of competition. Chapter II.P.2. cites the significance of these data in bid analysis.

(4) The Number of Change Orders. The number per contract of dollar-valued change orders is analyzed to determine the effect it has on the change order rate. Some change orders are "no-cost" and do not directly affect the change order rate. Among the dollar-valued change orders are amounts either added to, or deducted from, the contract price. This variable is of no value for predictive purposes, it is noted, since it cannot be known at the time of bid opening.

(5) Low Bid/Mean Bid Deviation. The deviation of the low bid from the mean bid can be expressed as a measure of the number of standard deviations that lie between the low bid and mean bid on a given contract. It conveniently normalizes all contracts regardless of award amount. A comparatively high value here is an indication of

an unusually deviant bid. But the value of a standard deviation is diminished for very small population sizes, so this measure is used only on contracts where there were at least four bidders. Analysis is focused on the determination of any relationships between this value and the change order rate.

(6) "Equivalent" Change Order Rate. A contract change order is frequently intended as a means of correcting a deficiency or mistake or making an "in scope" change that is more accommodating to the facility user. Frequently, a specific feature of a final facility after change orders is not that which was originally intended at the award of contract. In many cases, some facility features are no longer needed or are substituted by an equivalent "in-scope" alternative. These changes do not alter the function of the facility, but they do alter the contract price, and usually at a lower cost. Adding the amount of deductive change orders back into the contract price reflects more accurately what the contract would have cost if the original features were left intact. While this is not necessarily an accurate assumption for all deductive change order situations, it is believed to provide a more conservative comparison of contracts in the context of "dollar's worth" of construction. Value engineering change orders are not added back into the contract price, because this kind of change order actually reduces the contract price without "impairing essential functions or characteristics." The basic criterion for deducting the "equivalent" change order, as contrasted with leaving the Value Engineering change order intact, is in the consideration given to the Government. In the "equivalent" change order, the Government gets a reduction in the contract price, because it is buying something less in value than originally intended.

(7) Winning Bid to Average Bid Ratio. This value, usually less than unity (unless there is only one bidder), compares the relative difference between the winning bid and the competitive average. The "competitive average" excludes the winning bid in its computation and is assumed to be a more realistic approximation of a construction project's "true" or market price. Therefore, a low ratio would imply that a winning bid is priced far below expected costs, and is prone to being a "buy-in" or a potentially losing venture for the contractor.

(8) Winning Bid to Government Estimate Ratio. The use of this ratio for analysis assumes that the independent Government estimate, also referred to as the "engineer's estimate," is a fair price for the contract. The relationship of change order rates to this ratio is another focus of analysis.

b. Research Limitations

The availability of Scales of Bids and a source for reliable Government estimates is clearly the most limiting factor of this research. A reliable classification code for the type of construction performed under each contract was extremely limited. It is acknowledged that certain types of construction, such as placement of underground utilities, are inherently risky. Many projects involve an aggregation of various construction trade disciplines, so it is difficult to make a single, inclusive classification for a contract. NAVFAC Facility Category Codes [Ref. 35] are available in CMS for Military Construction contracts only. However, Facility Category Codes categorize contracts according to facility type rather than construction type. Table II summarizes the distribution of Military Construction contracts contained in the database according to Category Code.

TABLE II
MCOM Contracts by Category Code

<u>Facility Category</u>	<u>Number of Contracts</u>
Operational (excl. Waterfront)	21
Waterfront	10
Training	19
Maintenance	33
Production	1
Supply	12
Hospital, Medical and Dental	7
Administration	8
Unaccompanied Personnel Housing	9
Community	3
Utilities and Ground Improvements	43
<hr/>	
Total Military Construction Contracts in Database	173

c. Other Data

For informational purposes, Figures 2.2 and 3.1 show the trends in various measures of construction industry inflation and unemployment over Fiscal Years 1977 to 1982. This information is extracted from periodical issues of Engineering-News Record (ENR).

(1) Construction Industry Inflation. Figure 3.1 plots ENR's Construction Cost Index (CCI) for three major geographical areas pertinent to the database contracts. The CCI is a measure of the combined effect of wage and material price changes on the value of the construction dollar. The year 1967 was established as the base for an index value of 100. This index is computed monthly by ENR for twenty major U.S. metropolitan areas.

(2) Unemployment Rate. This rate is determined quarterly by ENR and is expressed as a national average; no geographical distinctions are made.

(3) Small Business Set-Asides. NAVFAC requires that all construction procurement in excess of \$2500 and under \$1,000,000 shall be considered for Small Business Administration (SBA) set-asides [Ref. 12: p. 4.2.13]. A small business set-aside is a procurement that is eligible only for award to an SBA-certified contractor. Set-asides were created to encourage more commerce among small, entrepreneurial firms. Approximately 95 percent of the database contracts are set-asides. The awarding of set-asides has drawn some concern:

A dilemma to the Government posed by set-asides is that in the short run, prices may be higher and competition restricted as small businesses incur high start-up costs and are unable to take advantage of economies of scale to lessen costs. In the long run, however, the set-aside program enlarges the total number of contractors available to compete, and it should thereby contribute to lower contract bids. [Ref. 37: p. 21]

B. ANALYTICAL COMPUTATIONS

The data were compiled for analysis on the IBM 3033AP Computer at the Naval Postgraduate School, Monterey, California. The general purpose statistical computing system, Minitab [Ref. 36], was used to perform various computational functions for data organization and analysis. The functions included:

- Sorting, rank-ordering, and recoding of data.
- Mathematical calculations (averages, totals, standard deviations, etc.).
- Histogram and plot construction.
- Regression analysis.
- Analysis of variance.

1. Sorting, Rank-ordering, and Recoding of Data

These features of Minitab are useful in examining ranges of values, breaking data into cells for variance analysis, and isolating selected independent variables for more detailed analysis. Variance and regression analyses can be performed conveniently for selected geographical areas, time frames, dollar ranges, facility types, and many other desired classifications.

2. Mathematical Calculations

Minitab enables simple calculations of averages, totals and standard deviations of various data diversifications. Much of the summary data represented in this study are the result of these calculations.

3. Histogram and Plot Construction

This feature provides convenient display of data distributions. Figure 3.2 displays the skewed distributions of change order rates for the database contracts. Plots afford graphical displays of relationships among variables. They are used, if necessary, in analysis of regression residuals to check the validity of the assumptions of normality and constant variance of the residuals. Plots are useful in visually displaying the degree of correlation between two variables.

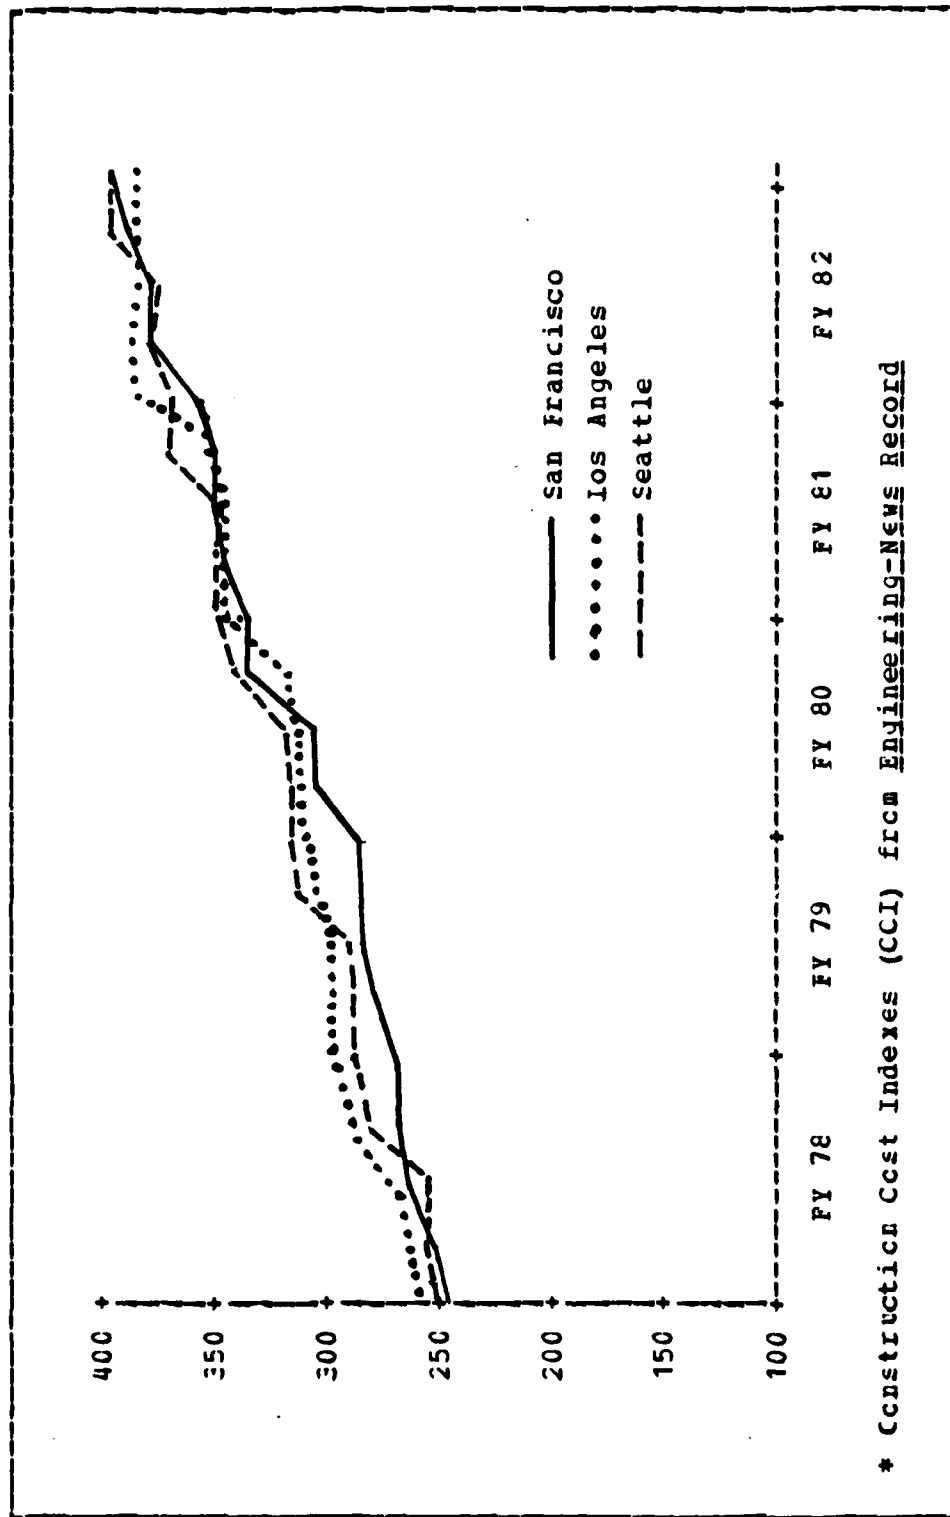


Figure 3.1 Construction Industry Inflation, Fiscal Years 1977-1982.

4. Regression Analysis

Regression analysis is a useful tool for determining relationships between a dependent variable and any number of independent variables. The change order rate, as a dependent variable, is examined for any significant relationship to a number of independent variables, such as number of bidders, the "spread," and bid-to-Government estimate ratio.

5. Analysis of Variance

Through the use of analysis of variance, significant differences among two or more populations of data can be tested. A statistical investigation can be made into the comparison of change order rates, for example, among different classifications of geographical areas, award periods, and bid-estimate ratios.

C. FINDINGS OF ANALYSIS

1. Dependent Variables

The objective of this analysis is to determine any significant relationships through regression and variance analyses between change order rates and other variables available in the database. Two independent variables are considered: the actual change order rate and the "equivalent" change order rate--a refined figure with the dampening effect of deductive change orders removed.

2. Independent Variables

The following are used as independent variables for regression analysis:

- Number of Change Orders.
- Number of Bids.

Actual Change Order Rate
Each * represents 2 observations

Middle of Number of
Interval Observations

0.00	minus 2	*
-2.00	7	****
0.00	70	*****
2.00	43	*****
4.00	40	*****
6.00	34	*****
8.00	24	*****
10.00	16	*****
12.00	14	*****
14.00	8	****
16.00	3	**
18.00	4	**
20.00	6	***
22.00	5	***
24.00	3	**
26.00	4	**
28.00	4	**
30.00	0	
32.00	2	*
34.00	1	*
36.00	3	**
38.00	1	*
40.00	plus 5	***

Equivalent Change Order Rate
Each * represents 2 observations

Middle of Number of
Interval Observations

-2.00	minus 1	*
0.00	72	*****
2.00	42	*****
4.00	40	*****
6.00	35	*****
8.00	24	*****
10.00	18	*****
12.00	14	*****
14.00	8	****
16.00	3	**
18.00	4	**
20.00	5	***
22.00	6	***
24.00	4	**
26.00	3	**
28.00	6	***
30.00	1	*
32.00	2	*
34.00	1	*
36.00	3	**
38.00	1	*
40.00	plus 7	****

Figure 3.2 Histograms of Change Order Rates.

- Number of Standard Deviations Between the Low Bid and the Mean Bid.
- Winning Bid to Mean Bid Ratio.
- Winning Bid to Government Estimate Ratio.
- Percent Spread Between the Low Bid and the Next Lowest Bid.

Subpopulations of the following variables were used for examining significant differences among change order rates through variance analysis:

- Award Date Periods, by fiscal year and by fiscal quarter.
- Award Amount, in stepped ranges of various dollar amount intervals.
- Geographical Area, by each of the eight categories, and then into two categories--"metropolitan" versus "rural."
- Funding source, in three cells--Military Construction, Non-appropriated Funds, and Operations and Maintenance.
- Number of Bids, in various cells ranging from one to 24 bids per contract.
- Winning Bid to Mean Bid Ratio, classified into 10 cells of approximate equal size:

0.00 - 0.70	0.88 - 0.91
0.70 - 0.78	0.91 - 0.93
0.78 - 0.82	0.93 - 0.95
0.82 - 0.85	0.95 - 0.97
0.85 - 0.88	0.97 - 1.00.

- Winning Bid to Government Estimate Ratio, classified into ten cells for all 300 contracts; and seven cells for the 173 MCON contracts:

<u>300 Contracts</u>	<u>173 MCON Contracts</u>
0.00 - 0.65	0.00 - 0.80
0.65 - 0.76	0.80 - 0.90
0.76 - 0.84	0.90 - 0.97
0.84 - 0.90	0.97 - 1.03
0.90 - 0.97	1.03 - 1.10
0.97 - 1.03	1.10 - 1.20
1.03 - 1.10	1.20 plus.
1.10 - 1.19	
1.19 - 1.30	
1.30 plus	

- Unemployment Rate, classified into 13 cells representing approximate construction industry unemployment rates ranging from 9.0 to 18.5 percent over 20 quarters.

3. Preliminary Findings

a. Change Order Rates

The change order rates for the data are shown in Table III. These rates are higher than the WESTDIV standards of six percent overall and five percent for Military

TABLE III
Change Order Rate Summary

Average Change Order Rate	Actual (percent)	Equivalent (percent)
MCON	7.83	8.43
CMN	7.53	8.41
NAF	6.19	6.23
OVERALL	7.62	8.29

Construction contracts. The WESTDIV standards are predicated upon the annual Work in Place, however, and do not account necessarily for all change orders to a given contract. The figures above are representative of a slightly different criterion, that is, the total change orders for each contract, including settlements to claims that may have lingered over a substantial period of the contract life. WESTDIV has been more successful in controlling the overall change order rate than it has the MCON change order rate. The Command Management Plan standards mentioned in Chapter II are high. The change order rates in Table III, it is recalled, were adjusted to eliminate deviant values. To make a more fair comparison between the performances of CMP-based change order rates and the change

order rates determined in this analysis, a number of factors would have to be considered in order to put them on an even plane. Such factors include the percentage of Work in Place contracts actually completed, and the average incidence rate of change orders toward the end of the contract life.

1. Number of Bids Affecting the "Spread"

Park [Ref. 15] asserts that the percentage spread decreases as the number of bidders increases. The evidence for this in this analysis is weak. The only significant¹⁷ difference in the spread is between the group of 3 to 5 bidders and the group of 6 or more bidders. The mean spread for the group of 3 to 5 bidders in the data is 13.2 percent, with a confidence interval between 10.1 and 16.3 percent. The mean "spread" for the group of 6 or more bidders is 6.9 percent, with a confidence interval between 4.4 and 9.4 percent. These findings are based on only 169 contract observations, as the "spread" was not calculated for contracts where there were three bidders or less.

4. Findings of Regression Analysis

A series of stepwise regressions were performed on each of the dependent variables against all considered independent variables. No single variable emerged with a correlation that was significant enough to explain the change order rate. The measure of the proportion of total variation in a dependent variable that is explained by a regression line is the coefficient of determination, or "r-squared" value.¹⁸ Each of the independent variables alone failed to yield a coefficient above 6.0 percent. The best

¹⁷Based on a 95 percent confidence level.

¹⁸The coefficient of determination or "r-squared" value can range from zero, which denotes no correlation, to unity, which represents perfect correlation.

fit found was a multiple regression of the bid-to-Government estimate ratio and the number of change orders against the actual change order rate. Only an 8.2 percent coefficient existed here with "t" ratios¹⁹ for the bid-to-Government estimate and number of change orders equal to -4.64 and 2.87 respectively. Since the values of the coefficients of determination are so close to zero, the change order rate explained by the independent variables is insignificant.

Subpopulations of geographical areas, funding sources and time frames failed to isolate any further data that could provide useful regressions. Plots of change order rates against each of the independent variables indicated that little resemblance of a linear relationship existed in any case. Figure 3.3, the plot of actual change order rate versus bid-to-Government estimate ratio, demonstrates this point.

5. Findings of Variance Analysis

In all analyses of variance, 95 percent confidence intervals for level means were assumed in hypothesis testing. One-way analyses of variance were performed for each of the two independent variables (actual and "equivalent" change order rates).

a. Award Date Periods

Two analyses of variance were performed: (1) by fiscal year and (2) by fiscal year quarter. If improvements have resulted in controlling change order rates due to WESTDIV efforts, then significant differences in change order rates should lie among the the five fiscal years. At least a significant difference between 1978 and 1982 should

¹⁹A "t" ratio should be at least plus or minus 2 to be considered significant enough for an independent variable to used in a regression equation.

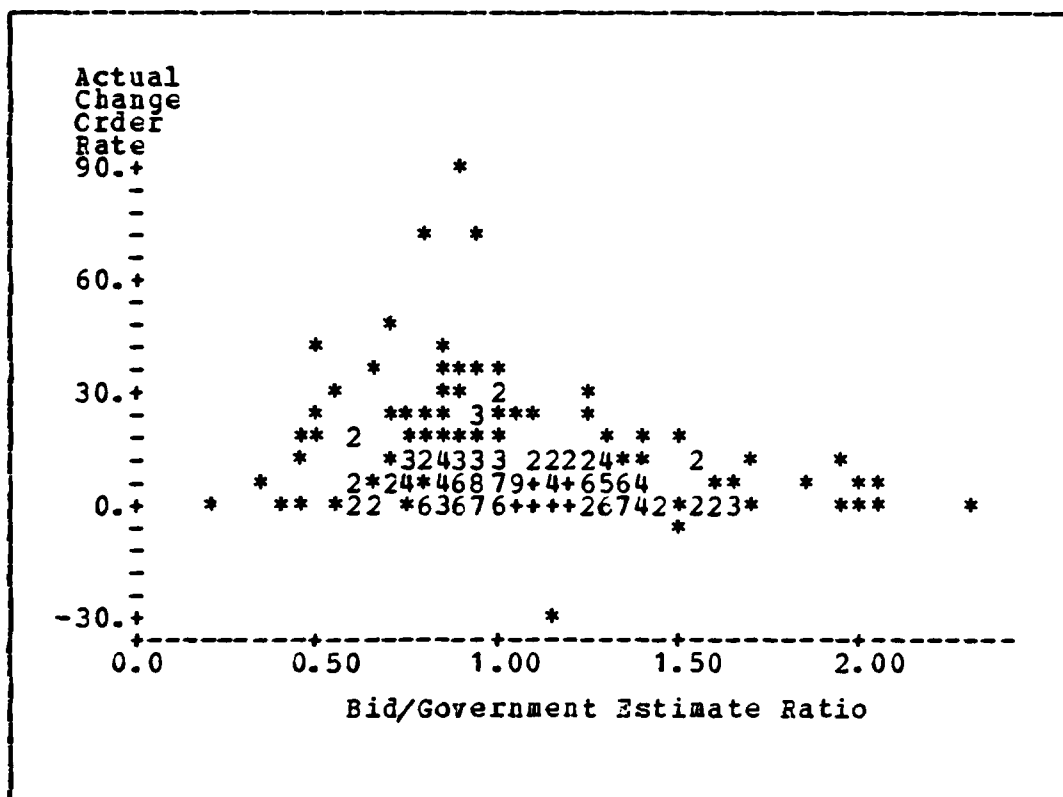


Figure 3.3 Plot of Change Order Rate vs. Bid/Govt Est.

exist. The hypothesis is that there has been significant improvement in reducing change order rates, and that it will be demonstrated by a change order rate confidence interval for 1982 that is below the lower limit of the confidence interval for 1978.

There is a common perception that contracts awarded in the fourth quarter tend to be "rushed" in the attempt to award before the end of the fiscal year and that the quality of specifications and drawings is therefore sacrificed. If this true, then a significantly higher change order rate should be seen for awards made during the fourth quarter in contrast to the other quarters. This

hypothesis will be affirmed if the lower limit of the fourth quarter change order rate confidence interval is greater than the upper confidence interval limits of the other quarters.

Analysis of variance for both cases reveals that no significant differences in change order rates can be found between any of the fiscal years or fiscal year quarters. Therefore, no improvement in reducing the WESTDIV change order rate over the five years was observed. Although there was no statistical difference in the change order rates among the four quarters, it was interesting to note that the mean change order rate (both actual and "equivalent") for contracts awarded during the fourth quarter was the lowest.

b. Other Findings

Analyses of variance for amounts of award, funding sources, number of bids, winning bid-to-mean bid ratios, Category Codes, and unemployment levels revealed no significant differences in change order rates among the various cells.

c. Geographical Areas

Among the eight described geographical areas there were no significant differences in change order rates between any two areas. An analysis of variance clearly shows that there is a significant difference in the change order rate between construction contracts performed in "rural" areas and those performed in the "metropolitan" or high density areas. Rural areas incur lower change order rates than do metropolitan areas. Figure 3.4 shows the 95 percent confidence intervals for each of these two cells. The upper limit of 7.1 percent for actual change order rate

(based on a pooled standard deviation) for rural areas is exceeded by the metropolitan areas' lower limit of 7.3 percent.

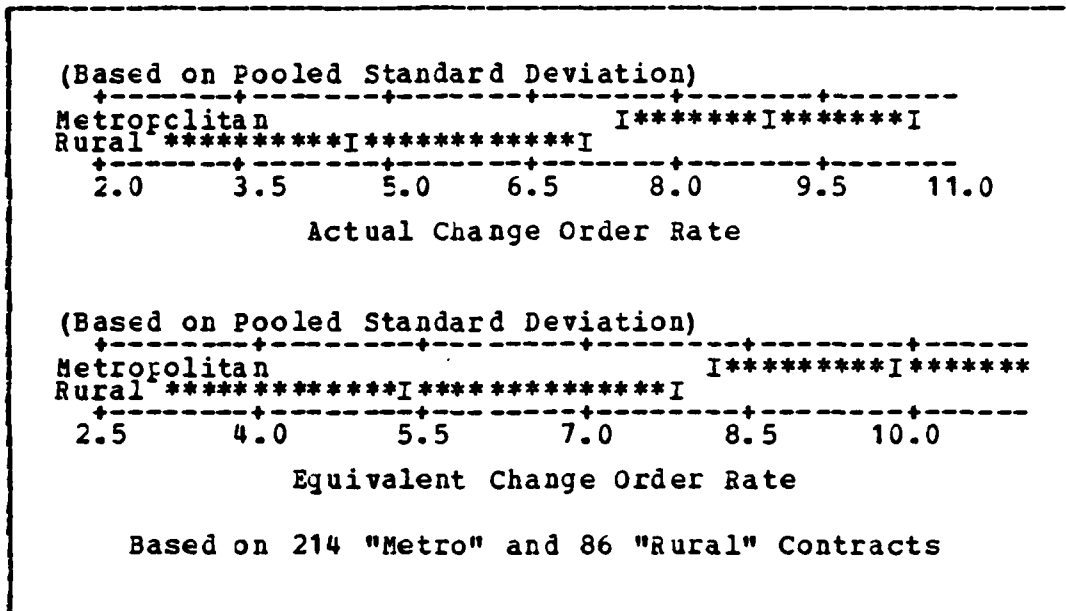


Figure 3.4 Variance Analysis for Geographical Areas.

d. Winning Bid to Government Estimate Ratio

The most significant findings in the difference among change order rates are found in the varying ranges of this ratio. Generally, it is found that change order rates tend to be high when the winning bid is proportionately lower than the Government estimate. Conversely, change order rates are significantly lower where the winning bid is much greater than or very close to the Government estimate. Figure 3.5 shows the 95 percent confidence intervals for change order rates among the cell classifications described

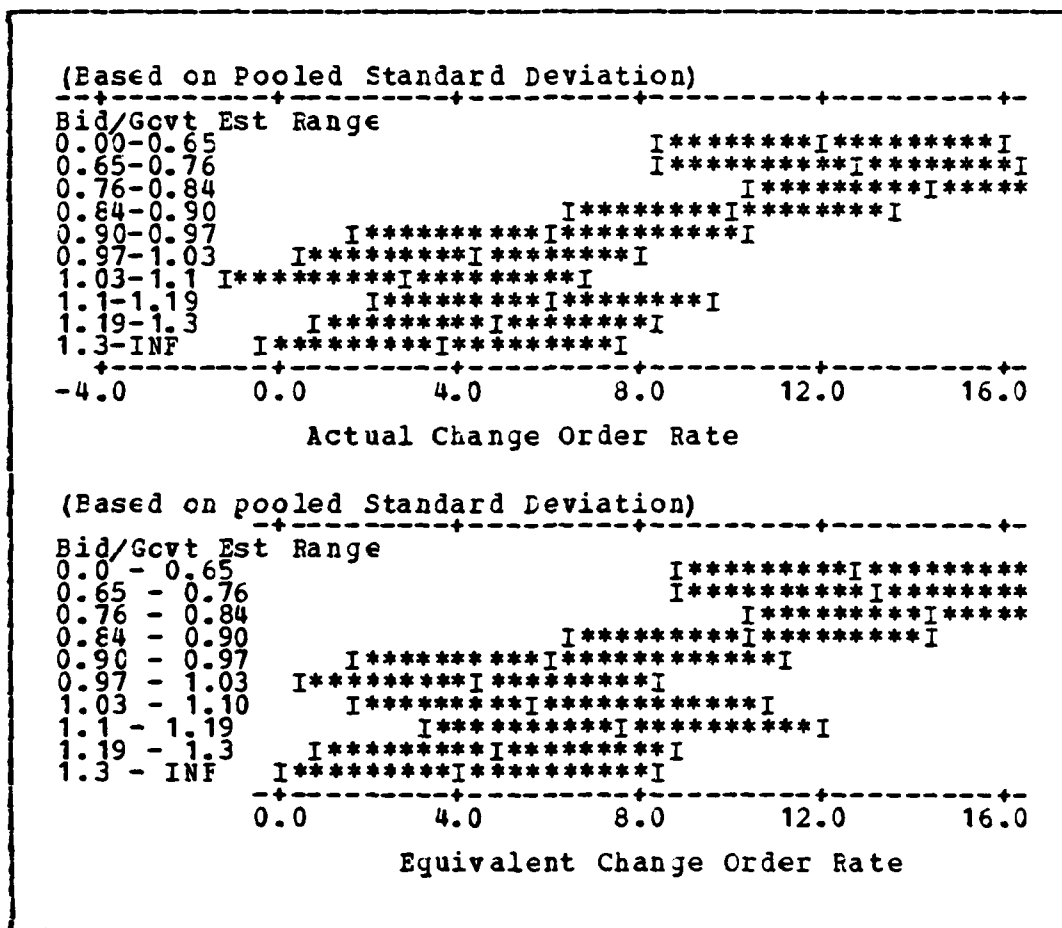


Figure 3.5 Variance Analysis for Bid/Govt Estimate.

in Section C.2. of this chapter. There is a significant difference in change order rates for both the actual and "equivalent" change order rate between the ratio extremes. The difference is significant between contracts where the ratio is 84 percent and lower; and where the ratio is either 119 percent and higher or between 97 and 103 percent. Where the ratio is roughly between 3 and 16 percent on either side of the Government estimate, no significant difference (at a 95 percent confidence level) in change order rates can be detected. One reason explaining why change order rates are

significantly low where the winning bid is within three percent of the Government estimate could be that these are considered "clean," risk-free jobs, and the work and costs involved are clearly discernable by both the Government and the contractor estimators.

This ratio may be of some use to the Contracting Officer in assessing the level of competition for a contract. If a contractor's bid is significantly lower than the Government estimate (approximately 15 percent), the likelihood of high change order rates can be anticipated.

D. SUMMARY OF ANALYSIS

A database with recent construction contract information was developed so that the principles introduced in Chapter II could be challenged for validity. It was necessary to make a number of refinements to the data so that various external influences such as nonserious bids, peculiar geographical characteristics, and terminated contracts that distort any general trends in change order rates could be eliminated.

A general statistical program, Minitab, was used to calculate a number of analytical determinations. Chapter II introduced the notion of competition intensity as a variable that affects the profit margin that contractors apply to bids. It is a general hypothesis of this thesis that as competition intensity increases, winning bidders tend to be contractors who are willing to assume greater risks than their rivals. They apply lean profit margins to their bids and expect change orders to ultimately improve their financial positions. The measures of competition intensity introduced in Chapter II, in addition to two measures introduced by the author, are applied in the database analysis to determine what conclusions can be drawn. Finally, the

incidence of change orders among varying classifications of geographical areas, time periods, price ranges, and unemployment rates was examined.

IV. SUMMARY AND CONCLUSIONS

A. SUMMARY

The excessive use of change orders in Government contracting has been alleged to be the result of improper diligence and care by management. The change order, in its original conception, was intended to be a remedy for the imperfections of contract language and depictions so that Government and contractor parties could proceed in executing the contract to a smooth end. Although change orders are intended primarily as a convenience for the Government so that "in-scope" modifications can be made to contract drawings and specifications, there is some evidence that the contractor has used change orders to his advantage. The intensity under which construction contracts are bid creates a highly competitive environment that demands a careful trade-off between a rational profit margin and a competitive price in order to win and stay in business.

It has been suggested that the winners of competitively-bid contracts are frequently contractors who fall into several categories: (1) they enjoy the advantage of economies of scale over their rivals, (2) they are more willing to assume certain risks, and (3) they see the opportunity to improve their financial positions, once the objective of winning the bid has been attained, by recouping losses through change orders. The limits that govern the extent to which contractors and contracting officers can use contract language to resolve issues of contract ambiguities in their favor have been defined through legal precedent.

Some of the theories and concepts of bidding strategy were applied to a model of representative construction contract data to test for their validities. Chapter II introduced three conventional measures for intensity of competition that were applied in the analyses. Risk-takers and "buy-in" bidders presumably emerge as victors in the bidding game under conditions of intense competition. For this reason, the number of bidders on a contract, the spread between low bidder and next lowest bidder, and the bid-to-Government estimate ratio were used in regression and variance analyses to determine the validity of this statement. Two other measures were introduced by the author for use in analysis: the bid-to-mean bid ratio and the number of standard deviations of the low bidder from the mean bid. Chapter III considered a number of predictive variables that might help to explain the conditions that affect change order rates.

It was necessary in the analysis to make several assumptions and refinements to the data. This was done so that the data could be analyzed without the influence of outliers to distort any general trends.

B. CONCLUSIONS

Change orders do not appear to be influenced by any dominant variable or combination of variables. There are many miscellaneous factors, apparently randomly distributed throughout the contract administration process, that contribute to contract price growth. These factors include, but are not limited to:

- Contracting officer and contractor expertise and competence.
- Availability of construction materials and labor.
- Architect-engineer competency.

- Contractor business windfalls or failures on other concurrent jobs.
- Backlog of contracting officer paperwork.

The results of analysis were conclusive. No direct relationship exists between the change order rate and any simple combination of variables. The most significant findings for the variables that were considered lie in the change order rates among varying bid-to-Government estimate ratios and geographical locations. Change order rates appear to be higher when the contractor bid is at least 15 percent below the Government estimate. When the contractor bid is very close (within three percent) to the Government estimate, or when his bid is approximately twenty percent above the Government estimate, change order rates are significantly lower. This information may be useful to the contracting officer in anticipating the magnitude of change orders for a contract, since it is information readily available at bid opening.

There is a significantly lower change order rate for construction contracts awarded for "rural" Naval activities than there is for contracts awarded in metropolitan areas, such as San Diego, Los Angeles, San Francisco, and Seattle/Bremerton. The explanation for this is speculative, but one may infer that "rural" contracts are "cleaner" or that the intense bidding competition in the metropolitan areas contributes to higher change order rates.

A discovery incident to the aim of this thesis was that the change order rate was remarkably similar to the spread. Of the 169 contracts with 4 or more bidders, the actual change order rate mean was 7.91 percent with a standard deviation of 12.10. The mean spread was 9.36 percent with a standard deviation of 13.06. These figures imply that

statistically, for a 95 percent confidence level, there is no significant difference between the two.

C. FUTURE RESEARCH

The intent of this thesis was to identify variables that significantly influence change order rates. Data was therefore refined so that general trends could be examined. One obvious shortcoming in the analyses was in the consideration given for the type (structural, electrical, mechanical, earthwork, etc.) of construction and the effect it has on the change order rate. Future research could explore this variable for significant relationships in change order occurrences.

There is room for more study on the performance of goal standards established in the NAVFAC Command Management Plan for controlling change orders. Research could not only determine how well the Engineering Field Divisions are performing under these standards, but it could identify where weaknesses exist. Such factors as geographical location, construction type, or type of facility may be selectively examined.

The analysis of bid spreads could determine when a justifiable move should be taken to cancel and rebid for contracts or when it is feasible to remain with a low bidder even if other forms of contracting (for example, negotiated fixed-price) seem desirable.

APPENDIX A
DESCRIPTION OF DATABASE VARIABLES

DATA GROUP 1

Column 1
CONTRACT NUMBER

The number assigned by WESTDIV prior to the Invitation for Bids (6-digit number), identifying the contract.

Column 2
AWARD DATE

The date the contract was awarded by WESTDIV to the contractor. (Year-Month-Day)

Column 3
AWARD AMOUNT

The amount of money originally awarded for a particular portion of work identified by line item in the CMS.

Column 4
GEOGRAPHY CODE

The location of construction, derived from the Unit Identification Codes listed for each contract in the CMS:

- 10 Metropolitan San Francisco area.
- 11 Northern California/Nevada area, excl. San Francisco metropolitan area.
- 20 Metropolitan Seattle/Bremerton area.
- 21 Washington/Oregon area excluding Seattle/Bremerton.
- 30 Metropolitan Los Angeles area.
- 31 Rural Los Angeles area, incl. Ventura County.
- 40 Metropolitan San Diego area.
- 41 Rural San Diego area, including Arizona.

Column 5
NUMBER OF BIDS

The number of responsive and serious bids submitted by contractors in response to the Invitation for Bids.

Column 6
MEAN BID

The average amount bid for each
contract, equal to:

Sum of bid amounts per contract
Number of bids per contract

Column 7
NUMBER OF CHANGE ORDERS

The number of dollar-valued
change orders to a contract.

DATA GROUP 2

Column 1 GOVERNMENT ESTIMATE

The independent estimate of construction made by the Government for work corresponding to the base bid and bid additives actually awarded.

Column 2 WINNING BID

The winning bid for the contract by the contractor, inclusive of all work segments and funding sources.

Column 3 WINNING BID TO MEAN BID RATIO

The ratio of the winning bid to the mean of bids for a contract. Values close to unity indicate relative closeness of the winning bid to the competition average.

Column 4 WINNING BID TO GOVERN- MENT ESTIMATE RATIO

The ratio of the winning bid to the Government Estimate. Values above unity indicate a winning bid that exceeds the Government Estimate.

Column 5 ACTUAL CHANGE ORDER RATE

The actual change order rate accounting for both additive and deductive change orders, expressed as a percentage:

$$\left(\frac{\text{Final contract price}}{\text{Original award amount}} - 1 \right) \times 100$$

Column 6 "EQUIVALENT" CHANGE ORDER RATE

The change order rate adjusted to dilute the effect of deductive change orders, and to account for the difference in the final product from the original, equal to:

$$\left(\frac{(\text{FCP} - \text{DCO's} + \text{VECO's})}{(\text{Original award amount})} - 1 \right) \times 100$$

FCP = Final contract price
DCO's = Deductive change orders
VECO's = Value Engineering change orders

DATA GROUP 3

Column 1
CONTRACT NUMBER

The number assigned by WESTDIV.
(This number can be used as a
cross-reference for data in the
first two Data Groups.)

Column 2
SECOND LOWEST BID

The amount submitted by the sec-
ond lowest bidder for the con-
tract.

Column 3
NUMBER OF STANDARD
DEVIATIONS OF LOW
BID FROM THE MEAN

The number of standard devia-
tions that the low bid for a
contract lies from the mean of
bids for that contract, ex-
pressed as:

$$\frac{(\text{Mean bid} - \text{winning bid})}{\text{Standard deviation of bids}}$$

Column 4
BID SPREAD

The percentage of spread between
the winning bid and the second
lowest bidder, expressed as:

$$\left(\frac{\text{Second lowest bid}}{\text{Winning bid}} - 1 \right) \times 100$$

Columns 5 and 6
ACTUAL CHANGE ORDER RATE and (As described in DATA
"EQUIVALENT" CHANGE ORDER RATE GROUP 1)

APPENDIX B
WESTDIV CCNSTRUCTION CONTRACTS DATA

Note: The following data are in three groups. The first two groups include data for all 300 contracts; the third group includes only those contracts with four or more bidders. The row number can be used as a cross-reference between the first two groups, and the Contract Number can be used as the cross-reference between the third group and the first two groups. For the first two groups, rows 1 through 173 are MCON contracts, 174 through 191 are NAF contracts, and 192 through 300 are OMN contracts. For the third group, 1 through 98 are MCON contracts, 99 through 110 are NAF contracts and rows 111 through 169 are OMN contracts.

DATA GROUP 1

Row	Contract Number	Award Date	Award Amount	Geog. Code	No. Bids	Mean Bid	No. C.O.
1	76-7344	77-10-28	708,297	21	5	780,542	6
2	76-7340	77-10-31	216,689	20	3	259,254	2
3	77-2067	77-11-03	389,225	20	3	478,195	13
4	76-7180	77-11-30	224,942	40	5	266,348	4
5	77-2276	77-12-01	367,000	31	6	460,632	2
6	76-7409	77-12-06	3,469,300	31	2	499,650	17
7	73-5370	77-12-06	3,379,000	20	2	3,271,000	11
8	77-2369	77-12-06	3,325,800	10	3	354,557	8
9	77-2454	77-12-09	269,000	40	3	297,333	1
10	76-7178	77-12-30	461,000	41	9	615,088	7
11	75-6305	77-12-30	555,000	31	8	7,001,945	12
12	77-2617	78-01-13	314,725	40	3	326,763	1
13	76-7336	78-01-19	711,868	10	3	958,533	37
14	76-7162	78-01-25	3,416,226	10	6	4,369,185	29
15	78-0224	78-02-06	3,345,430	10	2	3,351,185	3
16	77-2222	78-02-22	335,278	11	4	383,516	27
17	76-7150	78-02-28	5,982,800	40	6	6,175,274	2
18	77-2971	78-03-08	297,671	20	4	347,193	1
19	75-6468	78-03-15	4,031,967	10	5	5,377,916	23

201	223	245	267	289	301	323	345	367	389	401	423	445	467	489	501	523	545	567	589	601	623	645	667	689																	
71-4364	76-7328	77-2674	77-2657	77-2678	78-2738	77-2216	78-0243	75-0547	78-0539	78-2031	78-0073	77-2073	77-2043	76-2299	77-2057	77-2740	78-0638	77-2533	77-2554	77-2288	78-0081	77-2269	77-2136	77-2053	78-0093	78-0502	78-0870	78-0429	76-7142	74-3522	76-7022	76-7164									
78-03-17	78-03-31	78-04-21	78-05-01	78-05-03	78-05-26	78-06-15	78-06-23	78-06-28	78-06-30	78-08-02	78-08-04	78-08-16	78-09-11	78-09-15	78-09-22	78-09-26	78-09-29	78-09-29	78-10-23	78-11-14	78-11-29	78-11-29	78-11-30	78-11-30	78-12-05	78-12-15	78-12-21	78-12-29	78-12-29	79-01-15	79-01-18	79-01-24	79-02-07	79-02-15							
4599	4605	4534	4294	4191	4338	4282	4166	4055	4031	4037	4059	4079	4088	4096	4110	4179	4089	4096	4105	4130	4258	4258	4268	4261	4228	4250	4244	4288	4233	4337	4557	4652	4649								
1						3		2		11		1	2	4	1					4		1	6	3	3					1		7									
153	238	51	68	17	93	24	31	10	97	64	74	99	32	50	89	67	10	68	12	50	17	42	63																		
1																																									
527	160	327	311	350	392	306	494	959	945	320	297	682	092	809	009	317	698	216	891	358	363	279	456	752	834	478	288	044	214	403	763	349	324	518	492	816	770	553	808	547	
1								4				1	1	2	5	1							4		1	6	3	3													
88	33	73	22	50	00	49	78	28	47	95	50	26	44	41	68	88	46	50	23	13	38	71	87	60	10	26	20	16	50	65	15	50	39	29	0	15	39	0	48		
1																																									
34	57	26	97	54	35	54	35	54	35	27	32	41	10	36	46	42	33	57	32	27	54	53	52	44	93	71	3														

116	79-5400	79-09-09	20	00	2284	1	349	1	4
117	77-5401	79-09-09	20	00	2284	1	349	1	4
118	77-5402	79-09-09	20	00	2284	1	349	1	4
119	77-5403	79-09-09	20	00	2284	1	349	1	4
120	77-5404	79-09-09	20	00	2284	1	349	1	4
121	77-5405	79-09-09	20	00	2284	1	349	1	4
122	77-5406	79-09-09	20	00	2284	1	349	1	4
123	77-5407	79-09-09	20	00	2284	1	349	1	4
124	77-5408	79-09-09	20	00	2284	1	349	1	4
125	77-5409	79-09-09	20	00	2284	1	349	1	4
126	77-5410	79-09-09	20	00	2284	1	349	1	4
127	77-5411	79-09-09	20	00	2284	1	349	1	4
128	77-5412	79-09-09	20	00	2284	1	349	1	4
129	77-5413	79-09-09	20	00	2284	1	349	1	4
130	77-5414	79-09-09	20	00	2284	1	349	1	4
131	77-5415	79-09-09	20	00	2284	1	349	1	4
132	77-5416	79-09-09	20	00	2284	1	349	1	4
133	77-5417	79-09-09	20	00	2284	1	349	1	4
134	77-5418	79-09-09	20	00	2284	1	349	1	4
135	77-5419	79-09-09	20	00	2284	1	349	1	4
136	77-5420	79-09-09	20	00	2284	1	349	1	4
137	77-5421	79-09-09	20	00	2284	1	349	1	4
138	77-5422	79-09-09	20	00	2284	1	349	1	4
139	77-5423	79-09-09	20	00	2284	1	349	1	4
140	77-5424	79-09-09	20	00	2284	1	349	1	4
141	77-5425	79-09-09	20	00	2284	1	349	1	4
142	77-5426	79-09-09	20	00	2284	1	349	1	4
143	77-5427	79-09-09	20	00	2284	1	349	1	4
144	77-5428	79-09-09	20	00	2284	1	349	1	4
145	77-5429	79-09-09	20	00	2284	1	349	1	4
146	77-5430	79-09-09	20	00	2284	1	349	1	4
147	77-5431	79-09-09	20	00	2284	1	349	1	4
148	77-5432	79-09-09	20	00	2284	1	349	1	4
149	77-5433	79-09-09	20	00	2284	1	349	1	4
150	77-5434	79-09-09	20	00	2284	1	349	1	4
151	77-5435	79-09-09	20	00	2284	1	349	1	4
152	77-5436	79-09-09	20	00	2284	1	349	1	4
153	77-5437	79-09-09	20	00	2284	1	349	1	4
154	77-5438	79-09-09	20	00	2284	1	349	1	4
155	77-5439	79-09-09	20	00	2284	1	349	1	4
156	77-5440	79-09-09	20	00	2284	1	349	1	4
157	77-5441	79-09-09	20	00	2284	1	349	1	4
158	77-5442	79-09-09	20	00	2284	1	349	1	4
159	77-5443	79-09-09	20	00	2284	1	349	1	4
160	77-5444	79-09-09	20	00	2284	1	349	1	4
161	77-5445	79-09-09	20	00	2284	1	349	1	4
162	77-5446	79-09-09	20	00	2284	1	349	1	4
163	77-5447	79-09-09	20	00	2284	1	349	1	4

72

73

260	1110020411221010200204110212121212152132021	33	63742759614651547694845635664462713411191142925	11	27,327	8822-09-30	862	220
261		399		21	201,902	8822-09-30	8365	262
262		325		10	274,870	8822-09-30	1-0576	263
263		321		21	199,500	8822-09-30	1-0734	264
264		443		40	522,555	8822-09-30	2-5312	265
265		897		40	577,800	8822-09-30	2-0621	266
266		609		40	577,800	8822-09-30	2-0621	267
267		822		30	277,550	8822-09-30	2-0617	268
268		299		40	673,439	8822-09-30	2-0617	269
269		598		40	122,330	8822-09-30	2-0712	270
270		218		40	88,075	8822-09-30	2-0236	271
271		118		30	88,045	8822-09-30	2-0140	272
272		517		30	249,999	8822-09-30	2-0321	273
273		844		10	112,153	8822-09-30	2-0431	274
274		704		10	56,960	8822-09-30	2-0663	275
275		542		10	83,000	8822-09-30	2-0714	276
276		120		11	199,000	8822-09-30	2-0645	277
277		387		11	54,400	8822-09-30	2-0724	278
278		167		11	701,200	8822-09-30	2-0855	279
279		745		11	154,000	8822-09-30	2-0860	280
280		575		41	82,899	8822-09-30	2-0842	281
281		163		41	62,808	8822-09-30	2-0814	282
282		506		10	82,808	8822-09-30	2-0042	283
283		711		10	65,640	8822-09-30	2-0618	284
284		903		10	82,808	8822-09-30	2-0011	285
285		920		10	82,808	8822-09-30	2-0456	286
286		934		21	82,808	8822-09-30	2-0367	287
287		574		10	82,808	8822-09-30	2-0367	288
288		764		10	82,808	8822-09-30	2-0369	289
289		138		10	82,808	8822-09-30	2-0369	290
290		576		10	82,808	8822-09-30	2-0369	291
291		234		40	82,808	8822-09-30	2-0369	292
292		218		40	82,808	8822-09-30	2-0369	293
293		491		40	82,808	8822-09-30	2-0369	294
294		192		40	82,808	8822-09-30	2-0369	295
295		501		40	82,808	8822-09-30	2-0369	296
296		840		40	82,808	8822-09-30	2-0369	297
297		815		40	82,808	8822-09-30	2-0369	298
298		000		40	82,808	8822-09-30	2-0369	299
299		31		40	82,808	8822-09-30	2-0369	300

DATA GROUP 2

Row	Govmnt Estimate	Winning Bid	Win Bid/ Mean Bid	Win Bid/ Govt Est	Act Chg Ord'r Rt	Eqv Chg Ord'r Rt
1	635	708	0.90758	1.11506	2.6869	2.6869
2	222	216	0.85582	0.97377	1.41331	1.6849
3	330	389	0.81395	1.03793	8.55133	17.8467
4	366	224	0.84454	0.97546	6.55123	6.55123
5	443	367	0.79673	1.00273	10.9109	10.9109
6	461	469	0.99133	1.00764	41.5856	41.5856
7	362	379	0.91115	1.07574	12.1421	12.1421
8	344	269	0.91889	0.90000	0.0	0.0
9	626	461	0.90471	0.78039	32.1789	32.1789
10	422	555	0.94947	0.73619	2.4632	2.4632
11	431	314	0.93617	1.02044	0.0	0.0
12	815	711	0.95025	1.16867	23.5941	23.5941
13	366	345	0.93304	1.04237	27.5623	27.5623
14	815	335	0.98316	0.70938	3.5259	3.5259
15	366	382	0.87483	1.02585	26.7031	26.7031
16	557	335	0.87736	1.05650	24.0551	24.0551
17	856	397	0.86773	1.02164	26.7031	26.7031
18	190	203	0.87973	1.08322	26.0858	26.0858
19	525	468	0.88739	0.89227	1.1606	1.1606
20	158	599	0.87458	1.03842	16.5119	16.5119
21	538	605	0.76521	1.12428	10.9119	10.9119
22	541	249	0.86778	0.97744	3.6890	3.6890
23	211	253	0.84758	1.02438	9.5311	9.5311
24	537	294	0.90898	1.09905	6.4646	6.4646
25	387	333	0.84954	0.92371	13.4165	13.4165
26	349	333	0.84277	0.95587	2.5299	2.5299
27	318	282	0.82130	0.95587	2.0	2.0
28	395	282	0.82130	1.02164	2.0	2.0
29	318	282	0.82130	1.02164	2.0	2.0
30	395	282	0.82130	1.02164	2.0	2.0
31	395	282	0.82130	1.02164	2.0	2.0
32	395	282	0.82130	1.02164	2.0	2.0
33	395	282	0.82130	1.02164	2.0	2.0
34	395	282	0.82130	1.02164	2.0	2.0
35	395	282	0.82130	1.02164	2.0	2.0
36	395	282	0.82130	1.02164	2.0	2.0
37	395	282	0.82130	1.02164	2.0	2.0
38	395	282	0.82130	1.02164	2.0	2.0
39	395	282	0.82130	1.02164	2.0	2.0
40	395	282	0.82130	1.02164	2.0	2.0
41	395	282	0.82130	1.02164	2.0	2.0
42	395	282	0.82130	1.02164	2.0	2.0

76

[illegible]

[illegible]

187	2	010	000	43	180	92	000	000	129	5349	105	5349
188	0	110	000	421	622	160	000	000	000	8849	050	8849
189	0	110	000	492	042	042	000	000	000	5372	050	5372
190	0	389	500	412	132	132	000	000	000	0181	050	0181
191	0	605	000	387	778	778	000	000	000	0071	050	0071
192	0	430	000	977	375	375	000	000	000	0953	020	0953
193	0	700	000	847	703	703	000	000	000	5193	000	5193
194	0	499	500	311	153	153	000	000	000	8811	380	8811
195	0	358	500	312	706	706	000	000	000	1215	000	1215
196	0	217	800	977	400	400	000	000	000	0164	030	0164
197	0	117	400	966	330	330	000	000	000	1064	030	1064
198	0	577	400	722	110	110	000	000	000	1815	100	1815
199	0	577	400	722	505	505	000	000	000	1815	100	1815
200	0	207	723	262	307	307	000	000	000	5858	300	5858
201	0	107	000	167	505	505	000	000	000	0100	080	0100
202	0	140	000	580	307	307	000	000	000	9283	230	9283
203	0	198	000	239	800	800	000	000	000	5820	100	5820
204	0	232	000	399	290	290	000	000	000	7930	140	7930
205	0	337	400	466	220	220	000	000	000	7914	000	7914
206	0	333	000	548	965	965	000	000	000	3925	100	3925
207	0	323	000	318	773	773	000	000	000	1420	000	1420
208	0	276	000	371	900	900	000	000	000	5759	100	5759
209	0	333	000	349	007	007	000	000	000	0000	000	0000
210	0	333	000	87	499	499	000	000	000	0000	000	0000
211	0	333	000	233	900	900	000	000	000	0000	000	0000
212	0	333	000	170	000	000	000	000	000	0000	000	0000
213	0	656	000	233	600	600	000	000	000	0000	000	0000
214	0	242	000	144	350	350	000	000	000	0000	000	0000
215	0	136	620	144	900	900	000	000	000	0000	000	0000
216	0	778	900	103	160	160	000	000	000	3744	100	3744
217	0	222	000	144	350	350	000	000	000	0000	000	0000
218	0	106	000	861	700	700	000	000	000	5955	100	5955
219	0	497	000	461	200	200	000	000	000	3989	120	3989
220	0	539	000	461	200	200	000	000	000	0946	300	0946
221	0	450	000	461	200	200	000	000	000	0000	000	0000
222	0	432	000	461	200	200	000	000	000	0000	000	0000
223	0	660	000	461	200	200	000	000	000	0000	000	0000
224	0	326	000	461	200	200	000	000	000	0000	000	0000
225	0	326	000	461	200	200	000	000	000	0000	000	0000
226	0	502	000	461	200	200	000	000	000	9679	400	9679
227	0	136	100	461	200	200	000	000	000	3827	210	3827
228	0	740	200	461	200	200	000	000	000	0000	000	0000
229	0	900	200	461	200	200	000	000	000	8592	400	8592
230	0	150	000	461	200	200	000	000	000	4899	230	4899
231	0	271	000	461	200	200	000	000	000	9914	400	9914
232	0	337	000	461	200	200	000	000	000	2396	200	2396

[illegible]

282	93,000	82,200	0.70554	0.88387	8.8041	8.8041
283	146,000	192,887	0.93560	1.32114	3.5453	3.5453
284	190,100	185,808	0.85202	0.95236	0.04899	0.04899
285	671,000	682,820	0.45223	1.01762	1.9974	1.9974
286	420,000	433,651	0.90927	1.03254	0.8766	0.8766
287	148,000	98,641	0.71007	0.66549	17.8393	17.8393
288	42,300	81,410	0.61407	1.92459	7.8117	7.8117
289	1,010,000	527,916	0.79774	0.52269	1.5979	1.5979
290	66,900	47,750	0.78102	0.71375	12.6962	12.6962
291	740,000	520,101	0.61900	0.70284	10.6056	10.6056
292	88,100	98,576	1.00000	1.11891	10.6056	10.6056
293	790,000	3,471,960	0.80143	0.59965	35.7499	35.7499
294	821,000	634,003	0.74721	0.77227	37.2281	37.2281
295	303,000	153,400	0.68424	0.50627	22.2208	22.2208
296	181,900	146,900	0.82760	0.80759	0.0	0.0
297	32,900	24,000	0.80429	0.75000	12.1375	12.1375
298	35,400	25,600	0.71478	0.72316	15.0073	15.0073
299	46,600	67,600	0.55868	1.45064		
300	72,500	68,420	0.79266	0.94372		

DATA GROUP 3

Row	Contract Number	2nd Low Bid	No. Bid	Std Dev fm Mean	Bid Spread	Act Chg Ordrr Rt	Equiv Chg Ordrr Rt
1	76-7344	747,478	1	1.18900	5.516	2.6869	2.6869
2	76-7180	260,700	1	1.58300	15.897	6.5513	6.5513
3	77-2276	438,558	1	1.48500	19.498	6.5123	6.5123
4	76-7178	525,372	1	1.65700	13.964	32.1789	32.1789
5	75-6305	611,778	1	1.62300	0.866	2.4632	2.4632
6	76-7162	673,002	1	1.30500	1.962	27.0629	27.0629
7	77-2222	366,577	0	1.94300	9.335	3.1425	3.1425
8	77-7150	116,443	1	1.77300	2.744	26.0559	26.0559
9	77-2971	341,560	1	1.35400	14.744	4.7031	4.7031
10	75-6468	586,820	1	1.23900	23.682	26.0858	26.0858
11	76-7236	648,971	0	1.86000	3.061	29.0910	29.0910
12	76-7328	653,635	1	1.46400	8.039	10.5119	10.5119
13	77-2674	271,235	1	1.06200	8.856	13.6890	13.6890
14	77-2657	295,314	0	1.82200	0.193	6.4646	6.4646
15	77-2678	219,172	1	1.03700	0.046	13.4165	13.4165
16	78-0455	359,802	1	1.06200	7.854	2.2089	2.2089
17	78-2738	279,432	1	1.17900	22.555	0.2048	0.2048
18	77-2570	339,999	1	1.32300	20.524	10.7224	10.7224
19	78-0243	359,918	1	1.62900	6.034	7.5311	7.5311
20	75-6547	773,867	1	1.06300	5.406		

1	78-0539	14	352	1	105	11	0144	11	0143
2	77-2431	1	194	1	23900	2	9306	3	1783
3	77-2073	1	538	1	128700	3	3079	6	3385
4	76-7299	4	127	0	123500	4	6690	6	7403
5	77-2057	1	173	1	123500	1	2268	4	2268
6	78-0638	1	173	1	148400	5	0153	1	6294
7	78-0284	1	173	1	141300	5	0834	1	7837
8	78-0253	1	173	1	100700	5	7881	2	7740
9	77-2750	1	173	1	134000	2	6506	6	9570
10	77-2269	1	173	1	150500	5	0617	5	0617
11	77-2269	1	173	1	150500	0	1958	0	2220
12	78-0093	1	173	1	128700	19	0733	3	2212
13	78-0502	1	173	1	138700	6	2320	7	2320
14	75-6475	1	173	1	170200	2	0514	7	0514
15	78-0423	1	173	1	197600	20	6193	20	0142
16	76-7142	1	173	1	147600	6	4807	8	4807
17	76-3952	1	173	1	131600	8	1101	3	3488
18	75-6315	1	173	1	125200	6	1411	6	1411
19	77-2164	1	173	1	160200	13	7537	13	2326
20	77-2170	1	173	1	160200	14	8226	14	8226
21	77-2289	1	173	1	173300	15	2401	15	7621
22	77-2051	1	173	1	173300	3	2801	4	8422
23	77-2174	1	173	1	109200	5	9033	5	9422
24	78-0880	1	173	1	128600	12	8452	18	4220
25	77-2909	1	173	1	106400	5	5751	5	5751
26	77-2563	1	173	1	106400	4	9925	4	9925
27	79-2279	1	173	1	106400	5	1764	5	1764
28	77-2520	1	173	1	106400	5	4801	5	4801
29	78-0895	1	173	1	106400	5	2197	5	3079
30	78-0698	1	173	1	106400	3	0153	5	3079
31	79-2544	1	173	1	106400	7	1569	0	7786
32	78-0596	1	173	1	106400	2	0573	7	0573
33	77-2247	1	173	1	106400	0	9241	0	9241
34	79-5149	1	173	1	106400	1	2601	1	2601
35	77-2287	1	173	1	106400	1	1416	1	1416
36	79-5287	1	173	1	106400	2	8237	2	8237
37	78-0576	1	173	1	106400	8	8906	8	8906
38	76-7131	1	173	1	106400	7	9949	7	9949
39	78-0089	1	173	1	106400	1	1522	2	0550
40	78-0265	1	173	1	106400	2	7094	2	7094
41	76-7160	1	173	1	106400	9	3404	9	3404
42	75-6679	1	173	1	106400	5	7149	5	7149
43	79-5099	1	173	1	106400	0	1848	0	1848
44	77-2061	1	173	1	106400	1	2705	1	2705
45	79-5165	1	173	1	106400	1	3478	1	3478
46	77-5588	1	173	1	106400	3	5137	3	5137
47	79-2126	1	173	1	106400	10	5137	10	5137

117	79-001	0.97100	21.795	0.03827	12.3491
118	79-009	1.24300	18.782	21.2342	12.3491
119	145.039	1.33300	23.073	27.1124	12.3491
120	516.935	2.02200	15.910	47.2680	12.3491
121	60.777	0.92500	49.106	0.05619	12.3491
122	24.465	1.60700	29.452	16.5619	12.3491
123	18.399	1.22800	39.241	0.08862	12.3491
124	452.022	1.54100	8.757	30.2664	12.3491
125	71.303	1.11900	28.757	47.6777	12.3491
126	94.597	1.33100	15.119	5.6222	12.3491
127	028.532	2.00600	15.640	10.4371	12.3491
128	1.118	1.71200	16.251	13.1921	12.3491
129	129.986	1.34400	0.677	0.0723	12.3491
130	155.889	1.52700	4.638	31.0723	12.3491
131	186.841	1.10700	9.384	8.3117	12.3491
132	343.001	1.45000	7.984	0.0	12.3491
133	625.896	0.72500	3.659	0.7651	12.3491
134	110.007	1.55600	10.560	21.3115	12.3491
135	32.023	1.14300	18.880	4.7901	12.3491
136	476.486	1.05200	0.243	0.0	12.3491
137	253.958	1.32800	36.622	1.5773	12.3491
138	53.306	0.96100	14.011	0.03592	12.3491
139	61.481	1.47400	14.052	26.06828	12.3491
140	289.063	0.76000	1.325	20.6828	12.3491
141	706.027	1.31700	2.903	20.3945	12.3491
142	16.392	0.22500	4.845	23.3345	12.3491
143	223.452	1.47600	32.899	36.3747	12.3491
144	199.078	0.87600	4.283	8.0962	12.3491
145	77.990	1.34500	6.209	0.6358	12.3491
146	28.583	1.27200	18.368	0.05351	12.3491
147	65.254	1.01700	31.765	0.09071	12.3491
148	115.770	1.33900	19.923	0.0	12.3491
149	389.538	0.80800	12.150	0.05032	12.3491
150	224.188	1.30400	4.620	0.0	12.3491
151	58.001	1.10900	6.097	0.08041	12.3491
152	115.982	1.70100	41.823	8.5453	12.3491
153	194.474	1.04400	0.925	3.0	12.3491
154	91.750	1.02200	14.702	1.4899	12.3491
155	466.030	1.12600	6.619	0.9974	12.3491
156	123.132	1.20200	24.819	17.8766	12.3491
157	1.462	1.27500	6.142	3.8117	12.3491
158	462.485	1.30100	2.991	1.5979	12.3491
159	560.340	1.41200	23.548	12.6962	12.3491
160	649.178	1.67000	8.368	10.8237	12.3491
161	762.502	1.55500			12.3491
162					
163					
164					
165					
166					
167					
168					
169					
170					
171					
172					
173					
174					
175					
176					
177					
178					
179					
180					
181					
182					
183					
184					
185					
186					
187					
188					
189					
190					
191					
192					
193					
194					
195					
196					
197					
198					
199					
200					

35-7499
7-2281
3-8263
0-0
5-0073

35-7499
7-2281
3-8263
0-0
5-0073

7-829
3-806
15-044
20-273
14-643

1-68100
1-17700
1-10400
1-36700
1-47700

683,637
159,238
169,000
50,790
78,439

82-0700
82-0217
82-0207
82-0276
81-8709

165
166
167
168
169

LIST OF REFERENCES

1. Hanrahan, J. D., Government by Contract, W. W. Norton and Company, 1983.
2. U. S. Department of Transportation Report AD-DT-3-002, President's Council on Integrity and Efficiency Audit of Construction Contract Change Orders, 17 November 1982.
3. Yuspeh, I. "A Case for Increasing the Use of Competitive Procurement in the DOD," Bidding and Auctioning for Procurement and Allocation, FP. 104-128, New York University Press, 1976.
4. Weiss, W. H., "The Fallacy of Competitive Bidding," Government Executive, v. 8, pp. 38-39, February 1975.
5. Lytle, W., "The Fallacy of NOT Bidding Competitively," Government Executive, v. 8, pp. 40-41, February 1975.
6. Nash, R. C., Government Contract Changes, Federal Publications, 1975.
7. Gaskins, J. W., "Changed Conditions and Misrepresentation Under Government Contracts," Changes and Changed Conditions: Government Contracts Monograph No. 3, Federal Publications, pp. 14-25, 1962.
8. Nash, R. C. and Cibinic, J., Administration of Government Contracts, The George Washington University, 1981.
9. Whitesell, C. H., "Techniques of Negotiating Equitable Adjustments Under Government Construction Contracts," Changes and Changed Conditions: Government Contracts Monograph No. 3, Federal Publications, pp. 39-49, 1962.
10. Naval Facilities Engineering Command, Fiscal Year 1984 Command Management Plan, 1983.
11. Defense Audit Service Report 82-133, Report on the Audit of Construction Contract Change Orders, 25 August 1982.
12. Naval Facilities Engineering Command, NAVFAC Contracting Manual, Publication P-68, January 1979 (incl. changes).

13. Jones, R. R., Inordinate Use of Change Orders in Military Construction Contracts, Student Report, Leadership and Management Development Center, Air University, U.S. Air Force, 1983.
14. Adrian, J. J., Construction Estimating: An Accounting and Productivity Approach, Reston Publishing Company, 1982.
15. Park, W. R., The Strategy of Contracting For Profit, Prentice Hall Inc., 1966.
16. Kuhlman, J. M. and Johnson, S. R., "The Number of Competitors and Bid Prices," Southern Economic Journal, v. 50, pp. 213-220, July 1983.
17. Oppenheimer, S. P., Directing Construction For Profit, McGraw-Hill Book Company, 1971.
18. Carr, R. I., "Faying the Price for Construction Risk," Journal of the Construction Division, Proceedings of the American Society of Civil Engineers, v. 103, pp. 153-161, March 1977.
19. Engelbrecht-Wiggans, R., "Auctions and Bidding Models: A Survey," Management Science, v. 26, pp. 119-142, February 1980.
20. "Wrestling with Runaway Bidding," Engineering-News Record, v. 210, p. 70, 23 June 1983.
21. Dougherty, E. L. and Lohrenz, J., "Statistical Analyses of Bids for Federal Offshore Leases," Journal of Petroleum Technology, v. 28, pp. 1377-1390, November 1976.
22. Hohns, H. M., "How Can I Prevent the Dispute From Happening? How Can I Talk My Way Out of Trouble at the Job Site?" Avoiding Liability in Architecture, Design and Construction, pp. 305-314, John Wiley and Sons, 1983.
23. Sarkisian, S. S., "Contractor's Viewpoint of Navy Construction," Construction Management (text), U. S. Navy Civil Engineer Corps Officer School, pp. 2812-8 (1-11).
24. Howell, E. B. and Howell, R. P., Untangling the Web of Professional Liability, Design Professionals Insurance Company, 1976.
25. Vom Baur, F. T., "Differences Between Commercial Contracts and Government Contracts," The American Bar Association Journal, 1968.

26. Robertson, J., Selling to the Federal Government, McGraw-Hill Book Company, 1979.
27. Nash, R. C. and Cibinic, J., Federal Procurement Law, Volume II, The George Washington University, 1980.
28. Pettit, W. F., "Interpretation of Government Contracts: The Twelve Rules," The Government Contractor Briefing Papers, December 1965.
29. Stckes, M., Construction Law in Contractor's Language, McGraw-Hill Book Company, 1977.
30. The Government Contractor, v. 22, 6 October 1980, pp. 9-10.
31. The Government Contractor, v. 19, 3 January 1977, pp. 3-4.
32. Nash, R. C. and Cibinic, J., Federal Procurement Law, Volume II, The George Washington University, 1977.
33. Federal Acquisition Regulation, Volume I, Part 48.
34. Gilbreath, R. D., Managing Construction Contracts, John Wiley and Sons, 1983.
35. Naval Facilities Engineering Command, Department of the Navy Facilities Category Codes, Publication P-72, March 1977.
36. Ryan, T. A., Joiner, B. L. and Ryan, B. F., Minitab Reference Manual, Duxbury Press, 1981.
37. Lenk, B. R., Government Procurement Policy: A Survey of Strategies and Techniques, The George Washington University, 12 May 1977.

INITIAL DISTRIBUTION LIST

	No. Copies
1. Defense Technical Information Center Cameron Station Alexandria, Virginia 22314	2
2. Library, Code 0142 Naval Postgraduate School Monterey, California 93943	2
3. Defense Logistics Studies Information Exchange U. S. Army Logistics Management Center Fort Lee, Virginia 23801	1
4. Department Chairman, Code 54 Department of Administrative Science Naval Postgraduate School Monterey, California 93943	1
5. Assistant Professor Dan C. Boger, Code 54Bk Department of Administrative Science Naval Postgraduate School Monterey, California 93943	2
6. LCDR William R. Talutis, CEC, USN, Code 54Tu Department of Administrative Science Naval Postgraduate School Monterey, California 93943	1
7. Commander Naval Facilities Engineering Command 200 Stcvall Street Alexandria, Virginia 22332	1
8. Mr. J. M. Cowden, Code 09N Naval Facilities Engineering Command 200 Stcvall Street Alexandria, Virginia 22332	1
9. Commanding Officer Western Division Naval Facilities Engineering Command San Bruno, California 94066	2
10. Commanding Officer Naval School Civil Engineer Corps Officers Fort Huachuca, California 93043	1
11. LCDR James R. Rosmond, CEC, USN Resident Officer in Charge of Construction NAVFACENGCOM Contracts Andrews Air Force Base Washington, D. C. 20331	1

END

FILMED

3-85

DTIC
